



# ANALYSTLAB AFRICA

*Experience Lab Internship Programme*



## Week 1 of 4 - Understand & Plan

|                         |                                                                               |
|-------------------------|-------------------------------------------------------------------------------|
| <b>Intern Name</b>      | <b>Lamiaa SAMRAOUI</b>                                                        |
| <b>Track</b>            | <b>Project Management</b>                                                     |
| <b>Project</b>          | <b>FinTrust Financial Intelligence &amp; Digital Banking Support Solution</b> |
| <b>Week</b>             | <b>Week 1 of 4</b>                                                            |
| <b>Submission Date</b>  | <b>19 - 09 - 2026</b>                                                         |
| <b>Document Version</b> | <b>1.0</b>                                                                    |

*Note: FinTrust Digital Bank is a fictional organisation. All customer, transaction and risk-related information referenced in this document is synthetic and used for educational purposes only.*

# Table of CONTENT

|                                                                     |           |
|---------------------------------------------------------------------|-----------|
| <b>1. Executive Summary.....</b>                                    | <b>2</b>  |
| <b>2. Business Understanding, Resources and Track Planning.....</b> | <b>2</b>  |
| 2.1 Business Problem.....                                           | 2         |
| 2.2 Why the Problem is Important.....                               | 3         |
| 2.3 How the Project Management Track Contributes.....               | 3         |
| 2.4 Type of Output the PM Track Provides.....                       | 4         |
| 2.5 Resource Review.....                                            | 4         |
| 2.6 Track Objectives.....                                           | 5         |
| 2.7 Success Criteria.....                                           | 6         |
| 2.8 Initial Plan for Weeks 2–4.....                                 | 7         |
| <b>3. Project Management Deliverables.....</b>                      | <b>8</b>  |
| 3.1 Part A - Project Charter.....                                   | 8         |
| Project Title.....                                                  | 8         |
| Business Problem.....                                               | 8         |
| Objective.....                                                      | 8         |
| Scope.....                                                          | 9         |
| Stakeholders.....                                                   | 10        |
| Expected Outputs.....                                               | 11        |
| Success Criteria.....                                               | 11        |
| Assumptions.....                                                    | 12        |
| Constraints.....                                                    | 12        |
| 3.2 Part B - Work Breakdown Structure (WBS).....                    | 13        |
| Week 1 - Understand & Plan.....                                     | 13        |
| Week 2 - Analyse & Prepare.....                                     | 14        |
| Week 3 - Develop & Integrate.....                                   | 14        |
| Week 4 - Test, Refine & Present.....                                | 15        |
| 3.3 Part C - Four-Week Timeline.....                                | 16        |
| 3.4 Part D - Initial Dependency Register.....                       | 18        |
| 3.5 Part E - Risk Register.....                                     | 20        |
| 3.6 Part F - Reporting Plan.....                                    | 23        |
| <b>4. Conclusion.....</b>                                           | <b>25</b> |

## 1. Executive Summary

This Week 1 submission presents the initial project management plan for the FinTrust Digital Bank Experience Lab. The project brings together Data Analytics, Data Science, ML Engineering and Generative AI to address a common business problem around financial intelligence, risk-related decision support and digital customer support.

My role is to provide the planning and coordination structure needed to keep the five tracks aligned throughout the four-week project. This includes managing the timeline, dependencies, risks, integration activities and delivery readiness.

Week 1 is an individual preparation phase - no formal cross-track collaboration is required until Week 2. This submission therefore focuses on building the governance foundation (project charter, WBS, timeline, dependency register, risk register and reporting plan) that will guide coordination once collaborative work begins.

## 2. Business Understanding, Resources and Track Planning

### 2.1 Business Problem

FinTrust Digital Bank has customer and transaction data but lacks an integrated solution that can:

- Provide clear visibility into customer and transaction behaviour
- Identify potentially unusual or higher-risk transaction patterns
- Generate predictive insights to support risk-related decisions
- Operationalise analytical or machine-learning outputs into a usable workflow
- Provide customers with reliable digital support grounded in approved information

- Bring these capabilities together into one coherent business solution

## 2.2 Why the Problem is Important

The main challenge is not only developing each technical component, but making sure that the outputs can be used together. For example, analytical findings may inform the predictive modelling work, while the resulting model may later need to be incorporated into an ML workflow. If these hand-offs are not planned early, delays or integration problems may occur.

Project management is therefore important for keeping the work aligned with the four-week schedule and making these dependencies visible. Without that coordination, each track could produce something technically valid but disconnected from the wider solution.

## 2.3 How the Project Management Track Contributes

The PM track does not produce analytical, predictive or AI outputs directly. Instead, it provides the structure that allows the other four tracks to combine their work into a single FinTrust solution.

The PM contribution will focus on five areas:

- Scope and alignment: keep the different tracks working toward the same project objective.
- Planning: translate the four-week roadmap into activities, milestones and expected outputs.
- Dependencies: identify important hand-offs between tracks before they become blockers.
- Risk management: maintain visibility of delivery, data, technical and integration risks.
- Progress reporting: monitor status and communicate issues that require attention.

## 2.4 Type of Output the PM Track Provides

The PM track produces planning and coordination outputs rather than a technical product. For Week 1, these include the project charter, WBS, four-week timeline, dependency register, risk register and reporting plan. These will be used as working documents and updated as the project progresses.

## 2.5 Resource Review

The table below reviews the resources relevant to the Project Management track. The PM track does not perform the detailed technical analysis of these resources in Week 1. However, understanding their role is important for planning future hand-offs and dependencies between tracks.

| Resource                                    | What It Contains                                                                                                      | How It Will Be Used                                                                                                                | Limitations Identified                                                                                                                         |
|---------------------------------------------|-----------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------|
| <b>FinTrust Project Brief (PDF)</b>         | Business scenario, business problem, objectives, scope, stakeholders, success criteria, data/AI governance principles | Used as the master reference for the project charter, WBS and risk register to ensure alignment with the true scope of the project | Contains no dates, budget or named external stakeholders; charter fields for these are therefore marked as not applicable or assumption-based  |
| <b>FinTrust 4-Week Master Roadmap (PDF)</b> | Week-by-week phase names and the primary activities expected of each track in each of the four weeks                  | Used directly to build the WBS and the four-week timeline, and to identify realistic dependency points between tracks              | Describes activities at a high level only; does not specify exact calendar dates, so week-level deadlines in the timeline are assumption-based |

|                                                                                 |                                                                                                                  |                                                                                                                                                                                                               |                                                                                                                                                                             |
|---------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <b>Week 1 Official Weekly Assignment (PDF)</b>                                  | Week 1 requirements common to all tracks, and the track-specific task for each of the five tracks                | Used as the direct specification for every section of this submission                                                                                                                                         | None identified; the brief is clear and self-contained for Week 1 scope                                                                                                     |
| <b>FinTrust Customer Data.csv / Transaction Data.csv / Data Dictionary.xlsx</b> | Synthetic customer-level and transaction-level records, and field definitions/business meaning for both datasets | Not analysed directly by the PM track in Week 1. Referenced only indirectly, as the WBS and dependency register assume the DA and DS tracks will profile and use these files from Week 1 onward               | As a non-technical track in Week 1, the PM track has not opened or profiled these files; any statements about their content would be speculative and are therefore excluded |
| <b>FinTrust Financial Knowledge Base.docx</b>                                   | Approved knowledge source that the Generative AI track will ground its customer-support assistant on             | Not reviewed directly by the PM track. Its existence is used to plan the GenAI track's Week 1–2 activities in the WBS and to anticipate a possible PM ↔ GenAI dependency around assistant scope documentation | Content not reviewed by PM track in Week 1; limitations cannot be assessed from this track's perspective                                                                    |

## 2.6 Track Objectives

1. Set up a clear project structure covering scope, responsibilities, deliverables and success criteria.
2. Translate the four-week roadmap into a workable WBS and timeline that can be used to monitor progress.
3. Identify and track cross-track dependencies before formal collaboration

starts in Week 2.

4. Maintain a practical risk register covering delivery, technical, data and integration risks.
5. Establish a simple reporting process to monitor progress, blockers and upcoming actions.

## 2.7 Success Criteria

For Week 1, I will consider the PM plan successful if:

- The project charter accurately reflects the business problem, objectives, scope and success criteria stated in the Project Brief, with no invented facts.
- The WBS and timeline cover all five tracks and all four weeks, and are consistent with the activities described in the 4-Week Master Roadmap.
- The dependency register identifies plausible, specific dependencies (not generic statements) that can be validated once cross-track outputs exist from Week 2.
- The risk register identifies at least eight relevant risks, each with a probability, impact, mitigation and owner.
- The reporting plan gives a clear, workable cadence for monitoring progress that the other four tracks and I can realistically follow.
- The submission satisfies the assignment's assessment criteria: business/problem understanding, resource and data understanding, track-specific planning, quality of approach, critical thinking, and documentation/professionalism.

## 2.8 Initial Plan for Weeks 2–4

| Week   | Phase                  | Main Focus                                | PM Track Focus                                                                                                                                                                                                                                                                                                                                                                                          |
|--------|------------------------|-------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Week 2 | Analyse & Prepare      | Move from planning to active coordination | I will mainly monitor whether the planned outputs are being produced and whether the first cross-track hand-offs are happening as expected. I will track progress against the Week 1 charter and WBS, initiate the formal cross-track collaboration, update the dependency register as real outputs become available, update the risk register with any new risks, and issue the first progress report. |
| Week 3 | Develop and Integrate  | Integration and issue management          | The priority will be to identify gaps between the individual outputs and make sure issues affecting integration are raised early. I will coordinate cross-track integration, manage issues and scope changes as they arise, track validation evidence supplied by each track, and update the timeline and risk register based on integration progress.                                                  |
| Week 4 | Test, Refine & Present | Delivery readiness                        | I will focus on confirming that the technical outputs, documentation, validation evidence and presentations are complete before final submission. I will coordinate final end-to-end testing and refinement, confirm all five tracks' deliverables are complete and documented, manage presentation readiness, and document lessons learned.                                                            |

*ASSUMPTION: Exact calendar dates for Week 2–4 deadlines are not stated in the supplied materials. This plan assumes the same weekly cadence as Week 1*

*(submission due Sunday, 11:59 PM WAT each week) until AnalystLab Africa issues dates for later weeks.*

## 3. Project Management Deliverables

### 3.1 Part A - Project Charter

#### **Project Title**

FinTrust Financial Intelligence & Digital Banking Support Solution

#### **Business Problem**

FinTrust Digital Bank has customer and transaction data but lacks an integrated solution that provides clear visibility into customer and transaction behaviour, identifies potentially unusual or higher-risk transaction patterns, generates predictive insights to support risk-related decisions, operationalises analytical and machine-learning outputs into a usable workflow, and provides customers with reliable digital support grounded in approved information.

#### **Objective**

##### *Primary Objective:*

To develop an integrated data and AI solution that helps FinTrust Digital Bank understand customer and transaction behaviour, identify potential financial-risk patterns, support operational decision-making and improve digital customer support.

##### *Supporting Objectives:*

- Analyse financial and customer data
- Identify meaningful business trends and patterns
- Develop relevant KPIs and business insights
- Build and evaluate a predictive model for an appropriate risk-related problem

- Develop an operational workflow around the model
- Build a controlled GenAI customer-support capability
- Apply appropriate testing and validation
- Integrate outputs from multiple technical disciplines
- Communicate findings and recommendations professionally

## Scope

### *In Scope:*

**Data Analytics:** data exploration, cleaning, KPI development, customer/transaction analysis, dashboarding and business insights

**Data Science:** exploratory analysis, feature engineering, predictive modelling, model evaluation, error analysis and interpretation

**ML Engineering:** model/pipeline integration, data/model workflow, API or service concepts, testing and technical documentation

**Generative AI:** prompt engineering, knowledge integration, customer-support assistant, RAG/knowledge-retrieval concepts, evaluation and guardrails

**Project Management:** planning, WBS, timeline management, dependency management, risk management, coordination, integration and final delivery

### *Out of Scope:*

- Processing real customer banking information
- Connecting to real bank accounts or executing real financial transactions
- Providing personalised financial or investment advice
- Making real lending, fraud or account-opening decisions
- Deploying a production banking system

- Making regulatory or legal claims beyond the approved fictional project resources

## Stakeholders

| Stakeholder                                               | Interest                                                                               | Influence                                          | What They Need From PM                           |
|-----------------------------------------------------------|----------------------------------------------------------------------------------------|----------------------------------------------------|--------------------------------------------------|
| <b>AnalystLab Africa (Programme Owner)</b>                | High - sets assignment requirements, deadlines and assessment criteria                 | High - evaluates weekly submissions                | Weekly submissions on time; clear documentation  |
| <b>FinTrust Digital Bank (fictional business context)</b> | Medium - provides the business context and requirements the project is designed around | Low - cannot give feedback                         | Coherent final solution; no invented facts       |
| <b>Data Analytics Intern</b>                              | High - produces business intelligence, KPIs and dashboard outputs                      | Medium - feeds DS and GenAI                        | Timeline clarity; dependency hand-off dates      |
| <b>Data Science Intern</b>                                | High - produces the predictive risk model and related analysis                         | Medium - feeds MLE                                 | Clear requirements; access to DA findings        |
| <b>ML Engineering Intern</b>                              | High - operationalises the model and data workflow                                     | Medium - depends on DS outputs                     | Model interface clarity; integration checkpoints |
| <b>Generative AI Intern</b>                               | High - produces the knowledge-grounded customer-support assistant                      | Medium - depends on knowledge base and DA insights | Scope clarity; evaluation criteria               |

|                                         |                                                         |                              |                                         |
|-----------------------------------------|---------------------------------------------------------|------------------------------|-----------------------------------------|
| <b>Project Management Intern (self)</b> | High - plans, coordinates, tracks risk and dependencies | Medium - supports all tracks | Accurate status updates from all tracks |
|-----------------------------------------|---------------------------------------------------------|------------------------------|-----------------------------------------|

*ASSUMPTION: The supplied materials do not name individual people (e.g., a specific FinTrust manager or AnalystLab mentor). Stakeholders are therefore described by role, consistent with the Project Brief's Team Structure and the fictional nature of FinTrust.*

## Expected Outputs

By the end of Week 4, the project is expected to produce:

- A business intelligence/KPI dashboard (DA)
- A trained and evaluated predictive risk model (DS)
- An operational ML workflow with technical documentation (MLE)
- A knowledge-grounded customer-support assistant with an evaluation and safety plan (GenAI)
- A complete set of PM governance documents (charter, WBS, timeline, risk register, reporting records)
- Five individual recorded presentations.

## Success Criteria

- Business Understanding - the solution addresses a clearly defined FinTrust business problem
- Data & Technical Quality - data, analysis, models and technical components are appropriately developed and documented
- Integration - outputs from different tracks are connected and actually used
- Validation - the team tests its work and demonstrates improvements based on

## findings

- Responsible AI/Data Use - the team recognises limitations, avoids unsupported claims, and uses synthetic data appropriately
- Communication - the solution can be explained clearly to technical and non-technical stakeholders
- Portfolio Readiness - work is documented and presented to a professional standard

## Assumptions

- All interns have access to the tools recommended for their track (Excel, SQL, Python/Pandas, Power BI, Scikit-learn, Git/GitHub, etc.)
- Weekly submission deadlines follow the Week 1 pattern of Sunday, 11:59 PM WAT, unless AnalystLab Africa states otherwise
- All five tracks are staffed by individual interns working independently in Week 1, as stated in the assignment brief
- The datasets and knowledge base referenced in the brief are complete and available to the relevant tracks from Week 1 onward

## Constraints

- Fixed four-week project duration
- Only the approved, synthetic FinTrust resources may be used, unless an assignment explicitly permits another resource
- No formal cross-track collaboration is permitted/expected until Week 2
- The synthetic Risk\_Review\_Flag must not be treated as a real fraud determination
- The GenAI assistant must not invent FinTrust policies, fees, limits, timelines or procedures

- Each intern remains individually accountable for their own track deliverables and final presentation

### 3.2 Part B - Work Breakdown Structure (WBS)

The WBS below translates the Master Roadmap into track-level activities for the four-week project.

#### Week 1 - Understand & Plan

| Track              | Key Activities                                                                                                           |
|--------------------|--------------------------------------------------------------------------------------------------------------------------|
| Data Analytics     | Review customer and transaction data; assess data quality; define business questions and KPIs; plan dashboard            |
| Data Science       | Define predictive problem; assess Risk_Review_Flag; identify candidate features; develop hypotheses and modelling plan   |
| ML Engineering     | Define technical requirements; design ML workflow and architecture; plan repository and testing approach                 |
| Generative AI      | Review approved knowledge base; define assistant scope; identify supported/unsupported use cases; design evaluation plan |
| Project Management | Create project charter, WBS, timeline, initial dependencies, risk register and reporting plan (this submission)          |
| Final Integration  | Not applicable in Week 1 - no formal cross-track collaboration required                                                  |

## Week 2 - Analyse & Prepare

| Track                     | Key Activities                                                                                                                                                                                                                                                                     |
|---------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <b>Data Analytics</b>     | Clean and analyse data; develop SQL/Python analysis; identify patterns; begin dashboard; share meaningful findings. Deliver cleaned dataset + 3–5 initial findings by mid-week so DS can begin feature engineering; share data-quality issue log with PM for risk register update. |
| <b>Data Science</b>       | Perform EDA; prepare data; engineer features; establish baseline model; begin evaluation                                                                                                                                                                                           |
| <b>ML Engineering</b>     | Prepare project structure and pipeline components; establish reproducible workflow; begin technical testing                                                                                                                                                                        |
| <b>Generative AI</b>      | Develop prompts; build initial assistant; test grounding; begin evaluation against approved knowledge                                                                                                                                                                              |
| <b>Project Management</b> | Track progress; manage dependencies; coordinate formal cross-track collaboration; update risks and actions. Review hand-offs and confirm that exchanged outputs are usable by the receiving track.                                                                                 |
| <b>Final Integration</b>  | Formal collaboration begins - tracks start exchanging tangible outputs (e.g., DA findings to DS/GenAI)                                                                                                                                                                             |


## Week 3 - Develop & Integrate

| Track                 | Key Activities                                                                                  |
|-----------------------|-------------------------------------------------------------------------------------------------|
| <b>Data Analytics</b> | Complete dashboard; deepen analysis; validate findings; provide outputs for integration         |
| <b>Data Science</b>   | Train and compare models; conduct error analysis; refine approach; share relevant model outputs |

|                           |                                                                                                                                                                             |
|---------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <b>ML Engineering</b>     | Integrate model/pipeline; develop workflow or API/service component; test integration and resolve issues                                                                    |
| <b>Generative AI</b>      | Integrate knowledge/retrieval approach; evaluate responses; improve grounding, safety and escalation                                                                        |
| <b>Project Management</b> | Coordinate integration; manage issues/changes; track validation evidence and delivery readiness. Track integration issues and agree actions/owners for unresolved blockers. |
| <b>Final Integration</b>  | Cross-track outputs are combined into the developing FinTrust solution and validated                                                                                        |

#### **Week 4 - Test, Refine & Present**

| <b>Track</b>              | <b>Key Activities</b>                                                                                                                                                                                    |
|---------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <b>Data Analytics</b>     | Test dashboard; refine visuals and insights; finalise recommendations and portfolio documentation                                                                                                        |
| <b>Data Science</b>       | Final model evaluation; validate performance; document limitations; prepare final technical materials                                                                                                    |
| <b>ML Engineering</b>     | End-to-end technical testing; refine workflow; document implementation and final evidence                                                                                                                |
| <b>Generative AI</b>      | Final grounding and safety tests; refine assistant; document limitations and evaluation results                                                                                                          |
| <b>Project Management</b> | Coordinate final integration; confirm deliverables; manage presentation readiness; document lessons learned. Complete final delivery checklist and confirm readiness of documentation and presentations. |
| <b>Final Integration</b>  | Integrated solution is tested, refined and prepared for final presentation; each intern records a 5–10 minute presentation                                                                               |

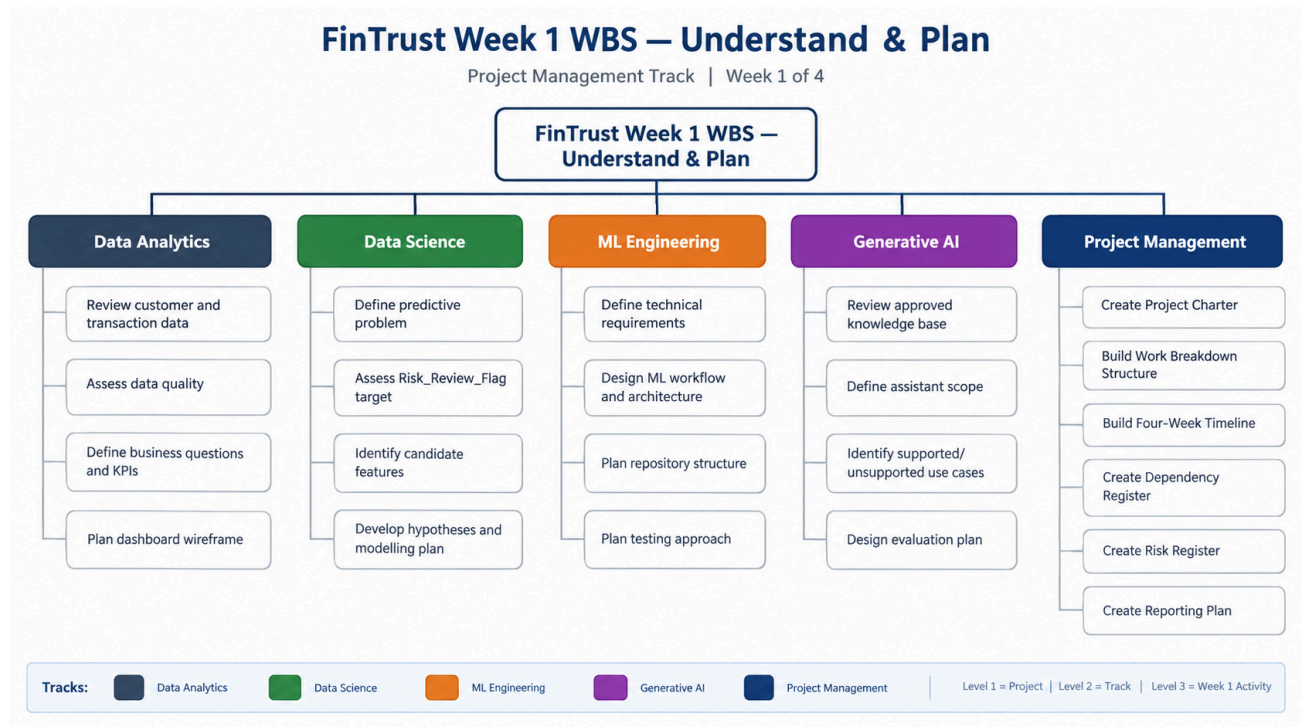

**Figure 1: Week 1 Work Breakdown Structure - Project Management Track**

This diagram shows the same WBS structure as the tables above in hierarchical form. The five branches correspond to the five tracks; the sub-nodes list each track's Week 1 activities.

### 3.3 Part C - Four-Week Timeline

| Week   | Phase              | Activity                                                                | Owner      | Milestone                                         | Deliverable                                                                                                                                                  | Deadline             |
|--------|--------------------|-------------------------------------------------------------------------|------------|---------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------|
| Week 1 | Underst and & Plan | Individual business, resource and track planning across all five tracks | All tracks | Week 1 planning documents complete for all tracks | Charter, WBS, timeline, dependency register, risk register, reporting plan (PM); business/resource understanding, objectives and Week 2–4 plans (all tracks) | Sunday, 11:59 PM WAT |

|               |                        |                                                                                                                                           |                        |                                                                                                         |                                                                                                                                                                                              |                      |
|---------------|------------------------|-------------------------------------------------------------------------------------------------------------------------------------------|------------------------|---------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------|
| <b>Week 2</b> | Analyse & Prepare      | Data analysis/EDA, feature engineering, prompt/assistant development, initial pipeline structure; formal cross-track collaboration begins | DA, DS, MLE, GenAI, PM | First cross-track outputs exchanged (e.g., DA findings shared with DS/GenAI)                            | Cleaned data & early findings (DA), baseline model (DS), pipeline structure (MLE), initial assistant (GenAI), updated risk/dependency register (PM)                                          | Sunday, 11:59 PM WAT |
| <b>Week 3</b> | Develop & Integrate    | Advanced development and cross-track integration; validation of outputs                                                                   | DA, DS, MLE, GenAI, PM | Model integrated into ML workflow; GenAI assistant grounded and evaluated; dashboard nearing completion | Near-final dashboard (DA), compared/refined models with error analysis (DS), integrated pipeline/service (MLE), evaluated assistant (GenAI), integration/risk tracking (PM)                  | Sunday, 11:59 PM WAT |
| <b>Week 4</b> | Test, Refine & Present | End-to-end testing, refinement, final integration and individual presentations                                                            | All tracks             | Integrated FinTrust solution finalised; all five individual presentations recorded                      | Final dashboard, final model documentation, final technical workflow, final assistant with safety/evaluation results, final PM documentation and lessons learned; 5 individual presentations | Sunday, 11:59 PM WAT |

*ASSUMPTION: The Week 1 assignment confirms a submission deadline of Sunday,*

11:59 PM WAT. Deadlines marked () for Weeks 2–4 assume the same weekly cadence, as exact dates for those weeks were not included in the supplied materials. Owner = track responsible for the activity. Individual intern names will be confirmed in Week 2.\*

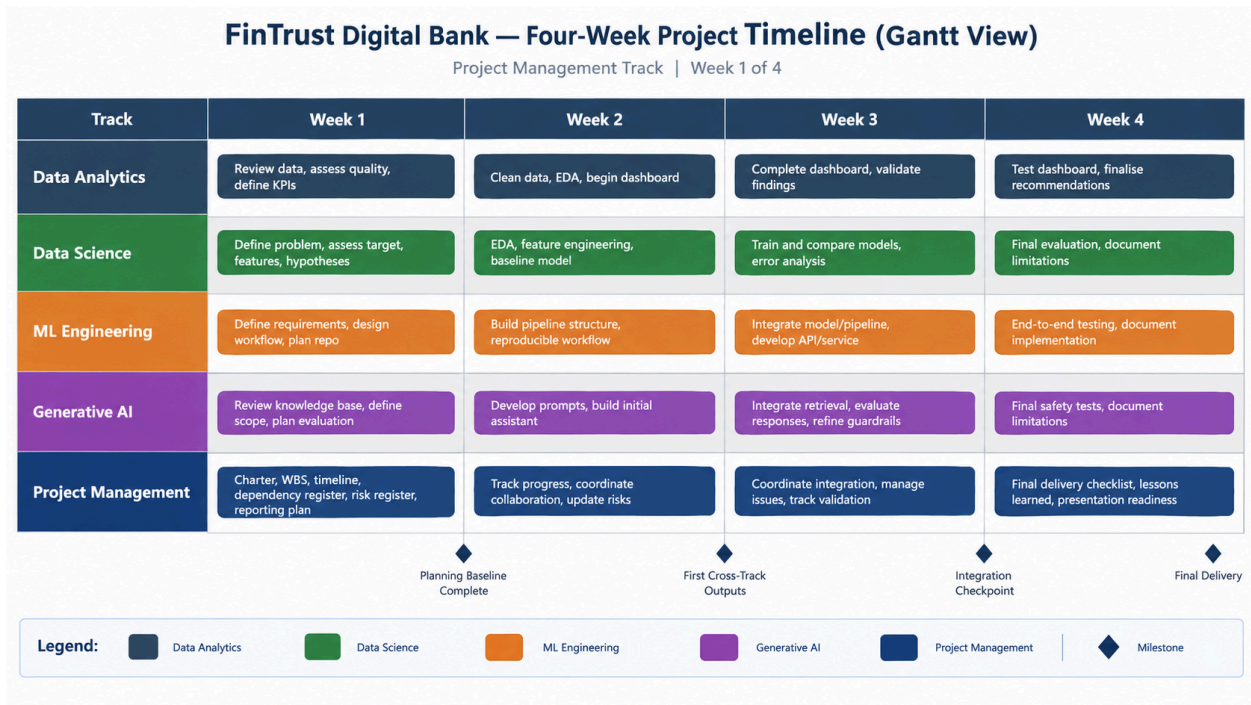


Figure 2: Four-Week Project Timeline (Gantt View)

The Gantt chart shows parallel activity across the five tracks. Diamond markers indicate weekly milestones: planning baseline (Week 1), first cross-track outputs (Week 2), integration checkpoint (Week 3) and final delivery (Week 4).

### 3.4 Part D - Initial Dependency Register

No formal collaboration is required in Week 1. The dependencies below are anticipated, based on the track roadmap, so that the team is prepared when formal collaboration begins in Week 2.

| ID     | Dependency From | Dependency To      | Why It May Matter                                                                                                                       | Expected Week |
|--------|-----------------|--------------------|-----------------------------------------------------------------------------------------------------------------------------------------|---------------|
| DEP-01 | Data Analytics  | Data Science       | DS's exploratory analysis and feature engineering may benefit from DA's early findings on transaction patterns and data-quality issues  | Week 2        |
| DEP-02 | Data Science    | ML Engineering     | MLE's pipeline and workflow design depend on DS's finalised feature set, baseline model and evaluation approach to integrate correctly  | Week 2–3      |
| DEP-03 | Data Science    | Project Management | PM needs visibility into DS's model progress and limitations to keep the timeline and risk register accurate                            | Week 2 onward |
| DEP-04 | ML Engineering  | Project Management | PM needs status on pipeline/API integration to track delivery readiness and flag integration risk early                                 | Week 3        |
| DEP-05 | Generative AI   | Project Management | PM needs the assistant's scope, use cases and safety/grounding plan to document expected outputs and risks accurately                   | Week 2        |
| DEP-06 | Generative AI   | Final Integration  | GenAI evaluation and safety results are needed to assess whether the assistant is ready to be included in the final integrated solution | Week 4        |

|               |            |                    |                                                                                                                                |               |
|---------------|------------|--------------------|--------------------------------------------------------------------------------------------------------------------------------|---------------|
| <b>DEP-07</b> | All Tracks | Project Management | PM needs each track's week-by-week outputs to keep the WBS, timeline, dependency register and risk register current            | Week 2 onward |
| <b>DEP-08</b> | All Tracks | Project Management | All tracks require a shared timeline and dependency visibility to coordinate hand-offs. PM provides this coordination function | Week 2 onward |

### 3.5 Part E - Risk Register

| <b>ID</b>   | <b>Risk</b>                                                                                                                            | <b>Probability</b> | <b>Rationale</b>                                                                                                             | <b>Impact</b> | <b>Mitigation</b>                                                                                                                 | <b>Owner</b>                  |
|-------------|----------------------------------------------------------------------------------------------------------------------------------------|--------------------|------------------------------------------------------------------------------------------------------------------------------|---------------|-----------------------------------------------------------------------------------------------------------------------------------|-------------------------------|
| <b>R-01</b> | Data-quality issues (missing values, inconsistent fields) in the synthetic datasets are not identified early, affecting DA and DS work | Medium             | Synthetic datasets often contain intentional quirks; neither DA nor DS has profiled the data yet                             | Medium        | Encourage DA/DS to complete a data-profiling pass in Week 1–2 before deep analysis; document known issues in shared notes         | Data Analytics / Data Science |
| <b>R-02</b> | One or more tracks fall behind schedule, delaying the start of formal collaboration in Week 2                                          | Medium             | Week 1 is individual work; Week 2 is the first time five interns coordinate. Coordination overhead typically peaks in Week 2 | High          | Track weekly deliverable completion against the WBS; flag slippage early and adjust the timeline or scope of Week 2 collaboration | Project Management            |

|             |                                                                                                                       |        |                                                                                                                              |        |                                                                                                                                                    |                    |
|-------------|-----------------------------------------------------------------------------------------------------------------------|--------|------------------------------------------------------------------------------------------------------------------------------|--------|----------------------------------------------------------------------------------------------------------------------------------------------------|--------------------|
| <b>R-03</b> | Dependencies between tracks (e.g., DS needing DA findings) are not communicated clearly once collaboration begins     | Medium | Five independent tracks have no shared communication channel yet; hand-offs are new                                          | Medium | Maintain and update the dependency register weekly from Week 2; PM to confirm hand-offs directly with each track                                   | Project Management |
| <b>R-04</b> | The predictive model's performance is limited by the size, balance or quality of the synthetic Risk_Review_Flag label | Medium | Synthetic labels are often imbalanced or weakly correlated with features; this is a known limitation of educational datasets | High   | Set realistic performance expectations in the DS modelling plan; document limitations transparently rather than overstating results                | Data Science       |
| <b>R-05</b> | The GenAI assistant produces ungrounded or hallucinated responses about FinTrust policies, fees or procedures         | Medium | LLMs are prone to hallucination when prompted outside their grounding data; the knowledge base has boundaries                | High   | Enforce the 'no invented policy' rule from the brief; build and run the 10+ evaluation questions specifically testing hallucination and escalation | Generative AI      |

|             |                                                                                                                             |        |                                                                                                                              |        |                                                                                                                                              |                             |
|-------------|-----------------------------------------------------------------------------------------------------------------------------|--------|------------------------------------------------------------------------------------------------------------------------------|--------|----------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------|
| <b>R-06</b> | Scope creep beyond the fictional, synthetic project boundaries (e.g., treating outputs as real financial advice)            | Low    | The project is framed as a realistic banking solution, which can blur the line between simulation and real-world application | Medium | Reinforce the Data & AI Governance Principles from the Project Brief in all track documentation and presentations                            | Project Management          |
| <b>R-07</b> | Individual interns lack access to, or familiarity with, a recommended tool (e.g., Power BI, Scikit-learn, Git)              | Low    | Tool access is assumed by the brief but not confirmed; interns have varying technical backgrounds                            | Medium | Confirm tool access at the start of each week; PM to note any access issues in the risk register and escalate to AnalystLab Africa if needed | Individual Track Owner / PM |
| <b>R-08</b> | The four-week duration, combined with individual accountability per track, leaves limited time to recover from early delays | Medium | Four weeks is a short window for five tracks to produce, integrate and present a coherent solution                           | High   | Use the Week 1 timeline and milestones to detect slippage as early as possible; keep Week 2–4 plans realistic rather than overly ambitious   | Project Management          |

|             |                                                                                                                                          |        |                                                                                                                       |        |                                                                                                                                                   |                                     |
|-------------|------------------------------------------------------------------------------------------------------------------------------------------|--------|-----------------------------------------------------------------------------------------------------------------------|--------|---------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------|
| <b>R-09</b> | Integration between tracks fails in Week 3 because outputs from different tracks are not compatible (e.g., data format, model interface) | Medium | Five tracks working independently may produce outputs that don't fit together without agreed formats                  | High   | Use the Week 1 dependency register to flag format/interface expectations early; PM to confirm compatibility checkpoints before Week 3 integration | Project Management / ML Engineering |
| <b>R-10</b> | Inconsistent documentation standards across tracks reduce the professionalism and portfolio-readiness of the final solution              | Low    | No shared documentation template has been agreed; each track may format outputs differently                           | Medium | PM to share a consistent documentation structure/template expectation and review deliverables for completeness before final submission            | Project Management                  |
| <b>R-11</b> | Unclear acceptance criteria for the final integrated solution                                                                            | Medium | The brief defines success criteria at a high level; specific evidence expected for each deliverable is not yet agreed | High   | Define expected evidence and final deliverables early, then review readiness during Week 3 rather than waiting until the final week               | Project Management                  |

### 3.6 Part F - Reporting Plan

I will use a lightweight weekly reporting process rather than creating a separate reporting structure for every activity. The aim is to keep progress, risks and dependencies visible without adding unnecessary administrative work.

Weekly submission checkpoint: Each track's official weekly assignment (due Sunday, 11:59 PM WAT) serves as the primary, verifiable progress checkpoint for that track.

WBS and timeline review: At the start of each week, the WBS and timeline are reviewed and updated to reflect actual progress from the previous week.

Dependency register review: From Week 2 onward, the dependency register is reviewed weekly to confirm which hand-offs between tracks are due, in progress, or completed.

Risk register review: The risk register is reviewed weekly; risk status (probability/impact) is updated, and new risks are added as they emerge, particularly around Week 2–3 integration.

End-of-week summary: A brief internal status note is kept for each week, covering deliverables completed, open dependencies, active risks and any blockers - feeding directly into the following week's submission.

Weekly Track Status: Each track will be reported using one of four statuses:

- On Track - activities are progressing as planned
- At Risk - potential delay or issue identified; mitigation in progress
- Blocked - activity cannot proceed without resolution
- Complete - deliverable finished and verified

Final reporting: In Week 4, progress reporting culminates in the individual 5–10 minute recorded presentation required by the Project Brief, summarising contribution, integration, results, limitations and lessons learned.

## 4. Conclusion

Week 1 has established the initial project structure for the FinTrust Experience Lab. The charter defines the scope and objectives, while the WBS and timeline provide the delivery baseline for the four-week project. The dependency and risk registers highlight areas that will require attention once formal cross-track collaboration begins in Week 2.

The plan is intentionally not treated as fixed. As the technical tracks produce tangible outputs, I expect some dependencies, risks and timelines to change. My focus in Weeks 2–4 will therefore be to keep the project aligned with its original objective while responding to issues that emerge during development and integration.

