



ANALYSTLAB AFRICA

Experience Lab Internship Programme

FinTrust Digital Bank

Financial Intelligence and Digital Banking Support Solution

Week 3 Submission — Project Management Track

Phase: Develop and Integrate



Field	Detail
Intern Name	Lamiaa SAMRAOUI
Track	Project Management
Project	FinTrust Financial Intelligence and Digital Banking Support Solution
Week	Week 3 of 4
Submission Date	3 October 2026
Document Version	1.0
Portfolio Repository	https://github.com/LamSa1/FinTrust-PM-Portfolio

Note: FinTrust Digital Bank is a fictional organisation. All customer, transaction and risk-related information referenced in this document is synthetic and used for educational purposes only.



Table of Contents

Monitoring Approach Note.....	3
Section 1 — Week 3 Project Summary.....	3
Section 2 — Progress Review (Part A).....	5
Section 3 — Integration Readiness Tracker (Part B).....	6
Section 4 — Updated Risk Register (Part C).....	9
Section 5 — Updated Issue Log (Part D).....	11
Section 6 — Change and Decision Log (Part E).....	12
Section 7 — Week 4 Readiness Plan (Part F).....	14
Section 8 — Week 3 Status Report.....	15
Section 9 — Validation and Refinement Evidence.....	17
Section 10 — Week 1 and 2 Assumptions Status Update.....	18
Section 11 — Limitations.....	18
Section 12 — Conclusion.....	19



Monitoring Approach Note

Week 3 continues the individual preparation phase. No formal cross-track collaboration is required. This submission monitors the project at two levels:

1. PM track outputs, which are stated as fact and are directly verifiable from this submission.
2. Project-wide integration readiness, which is assessed from public sources (LinkedIn posts and GitHub repositories) and clearly labelled as “Reported” or “Reviewed.” No cross-track status reaches “Confirmed” or “Validated” in Week 3.

The Week 3 brief confirms that individual responsibility is primary and that no formal collaboration is required. Public sources were used where available. No direct contact with any contributor was attempted or required.

Section 1 — Week 3 Project Summary

1. What I planned to accomplish in Week 3

In Week 2, I established the execution monitoring foundation: progress tracker, updated risk register, issue log, dependency register, decision log and status report. For Week 3, I planned to assess integration readiness across all five tracks, update governance documents with Week 3 findings, and produce a clear Week 4 readiness plan for final testing, refinement and presentation.

2. What I completed

- Reviewed Week 2 outputs and identified three areas requiring improvement
- Created an evidence-based Integration Readiness Tracker covering all five tracks
- Updated the Risk Register with Week 3 statuses, added two new risks (R-14 and R-15)
- Updated the Issue Log with Week 3 issues and resolutions
- Created a Change and Decision Log covering Weeks 2 and 3
- Produced a Week 4 Readiness Plan
- Prepared a Week 3 Status Report
- Demonstrated one meaningful validation and refinement cycle (see Section 9)
- Documented testing and refinement evidence

3. Major development activities

- Assessment of integration readiness for all five tracks using public sources
- Risk re-assessment based on Week 3 brief requirements



- Decision logging for Week 2 to Week 3 changes
- Preparation of Week 4 Readiness Plan covering testing, refinement, documentation, integration and presentation

4. Key findings and results

- Four of five tracks are reported or reviewed as complete, based on public sources
- No cross-track item reaches “Confirmed” or “Validated” status
- One track (Generative AI) has no public Week 3 evidence available
- The DA to DS hand-off (DEP-01) is reported as complete based on public sources
- The DS to MLE hand-off (DEP-02) is reported as on track
- Project health remains At Risk, trending toward On Track if Week 4 mitigations hold

5. Testing and validation performed

See Section 9 for the full validation cycle. In summary:

- Initial Output: Week 2 Risk Register with 13 risks
- Test: Reviewed against Week 3 brief requirements and available public sources
- Finding: Six risks resolved, three changed in status, two new risks identified (R-14 and R-15)
- Refinement: Updated register with Week 3 statuses; added R-14 and R-15 with documented rationale
- Re-test: Reviewed updated register against Week 3 integration requirements
- Result: Risk Register now reflects Week 3 project state accurately with 15 risks tracked

6. Improvements made

- Integration Readiness Tracker with evidence levels (Reported, Reviewed, Confirmed, Validated)
- Week 4 Readiness Plan (new deliverable)
- Change and Decision Log covering Weeks 2 and 3
- Updated Risk Register with 15 risks and honest evidence labels
- Separation of “completed output” from “integration readiness”

7. Major challenges

- Limited cross-track visibility in Week 3 (expected per brief)
- Assessing integration readiness without direct confirmation from track members
- Distinguishing “reported completion” from “confirmed integration readiness”
- No public Week 3 evidence found for the Generative AI track

8. Important decisions

See Section 6 (Change and Decision Log). Key decisions:

- Assessed four of five tracks as Reported or Reviewed complete



- Flagged Generative AI as Not Confirmed (no public evidence)
- Adopted “Reported and Reviewed” framing instead of “Confirmed and Validated”
- Added R-14 (Week 4 time compression) and R-15 (integration readiness not confirmed)
- Did not attempt direct contact with cross-track contributors, per Week 3 brief

9. Remaining limitations

- Integration readiness assessments are based on public LinkedIn posts and GitHub repositories, not direct confirmation
- No cross-track status reaches “Confirmed” or “Validated”
- Two ML Engineering sources were found and documented separately; their relationship is not confirmed
- No public Week 3 evidence found for the Generative AI track

10. What must be completed in Week 4

- Attempt direct confirmation of integration readiness if formal collaboration begins
- Final testing of all governance documents
- Final refinement of risk and issue registers
- Completion of Week 4 final documentation
- Preparation for individual 5 to 10 minute recorded presentation
- Final submission to Google Drive and GitHub

11. Final-week priorities

1. Confirm cross-track outputs where possible
2. Validate Week 3 assessments against any new information
3. Finalise risk register with Week 4 statuses
4. Complete end-to-end documentation review
5. Prepare and record the individual presentation
6. Final submission across all required channels

Section 2 — Progress Review (Part A)

Category	Status	Details
Completed Work	Complete	Week 1 governance foundation; Week 2 execution monitoring; Week 3 integration readiness assessment
Incomplete Work	Pending	Cross-track output validation (deferred to Week 4 per Week 3 policy)
Delayed Work	Minimal	DA dashboard completion reported complete per public sources



Major Achievements	Complete	All PM deliverables completed on schedule across three weeks; risk register matured from 11 to 15 risks; three consecutive on-time submissions
Remaining Activities	Pending	Week 4: final testing, refinement, documentation, presentation

Section 3 — Integration Readiness Tracker (Part B)

Evidence Levels Used in This Tracker

- **Reported:** Contributor publicly stated completion (LinkedIn post)
- **Reviewed:** PM accessed and reviewed the public output (GitHub)
- **Confirmed:** Track member directly confirmed to PM (none in Week 3)
- **Validated:** Integration tested and verified (none in Week 3)

No formal collaboration was required in Week 3. All cross-track evidence is from public sources. No direct contact was made with any contributor.

Integration Readiness Tracker

Track	Contributor	Main Week 3 Output	Status	Integration Readiness	Evidence Source	Outstanding Work
Data Analytics	Samuel Gichangi	Advanced SQL, Python analytics, custom dashboard, 5 validated findings, 5 recommendations	Reported Complete and Reviewed	Not Confirmed	Public LinkedIn post and shared DA documentation	Integration readiness not explicitly stated; final dashboard polish pending Week 4
Data Science	Unotidashe Jacob Hove	Model validated; code pushed to GitHub	Reported Complete and Reviewed	Not Confirmed	LinkedIn post and GitHub repository	Integration readiness not stated; Week 4 validation pending



ML Engineering	Zaid HARBOUL	Reported completion with integration reference	Reported Complete	Reported Integration-Ready (self-stated)	Public LinkedIn post	Independent validation pending
ML Engineering (alternative)	Charlez023	Full Week 3 repository: code, 20 tests, FastAPI /predict endpoint	Reviewed Complete	Not Confirmed	Public GitHub repository	End-to-end validation pending per repository README
Generative AI	No public source found	Not available	Not Confirmed	Not Confirmed	No public source available	All information
Project Management	Lamiaa SAMRA OUI (self)	All Week 3 PM deliverables	Complete	Ready	This submission	Final documentation and presentation in Week 4

Summary Assessment

- One track (Project Management) is Ready for Integration
- One track (ML Engineering via Zaid HARBOUL) is Reported integration-ready by the contributor — self-stated, not independently validated
- Two tracks (Data Analytics, Data Science) are Reported Complete and Reviewed based on public and shared documentation; integration readiness is not confirmed
- One alternative ML Engineering repository (Charlez023) is Reviewed Complete; integration readiness is not confirmed
- One track (Generative AI) has no public Week 3 evidence available
- Zero tracks reach “Confirmed” or “Validated” level

Evidence Sources — Full Detail

Data Analytics — Samuel Gichangi

Public LinkedIn post reporting Week 3 deliverables, plus a shared DA documentation file describing: advanced SQL analysis using JOINS, GROUP BY, CASE statements, subqueries, CTEs, aggregate functions and window functions; expanded Python analysis with 5+ visualizations; a custom analytical dashboard (mobile app dominance at 42.5% of volume; segment distributions across Everyday, Premium, Student, SME; risk density metrics); 5 empirically validated business findings; and 5 management recommendations. Integration readiness not explicitly stated.

Data Science — Unotidashe Jacob Hove



Public LinkedIn posts and GitHub repository (ANALYSTLAB-JACOB-INTERNSHIP-FINTECHBANK) showing validated model development and code. Integration readiness not explicitly stated.

ML Engineering — Zaid HARBOUL

Public LinkedIn post reporting completion with reference to integration readiness. Self-stated; independent validation pending.

ML Engineering (alternative) — Charlez2023

GitHub repository (FinTrust-ML-Engineering) containing Week 3 development: additional transaction features, model comparison (Logistic Regression and Random Forest), FastAPI /predict endpoint, 20 automated tests (all passing), and complete ML pipeline. Integration readiness not explicitly stated.

Generative AI

No public Week 3 source found. Status marked Not Confirmed.

Project Management — Lamiaa SAMRAOUI

This submission. All Week 3 deliverables completed.

Trello Board

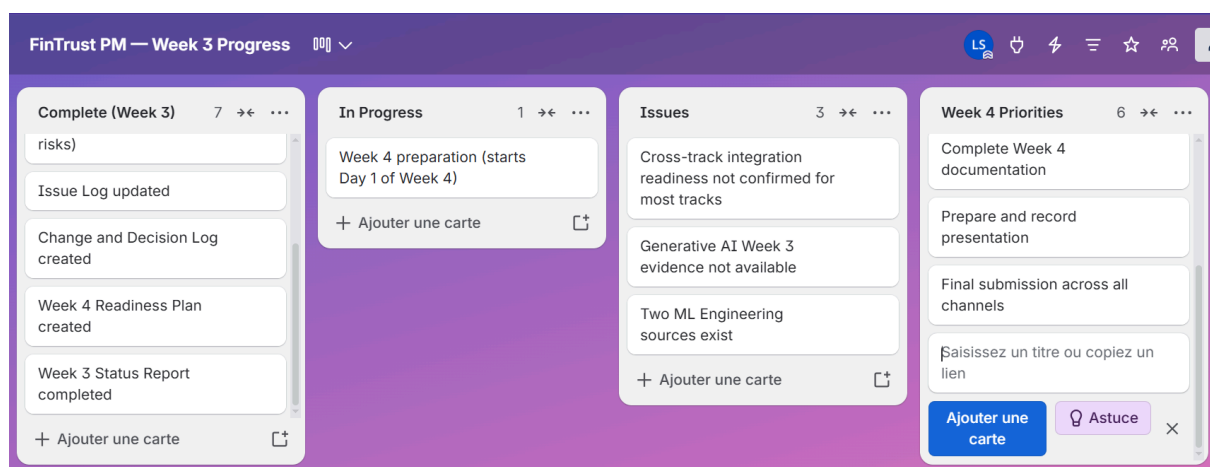


Figure 1: Trello Board — FinTrust PM Week 3 Progress

The board shows completed Week 3 deliverables, current issues, and Week 4 priorities. Screenshot taken during Week 3.

Integration Readiness Dashboard



Week 3 Integration Readiness — FinTrust Digital Bank

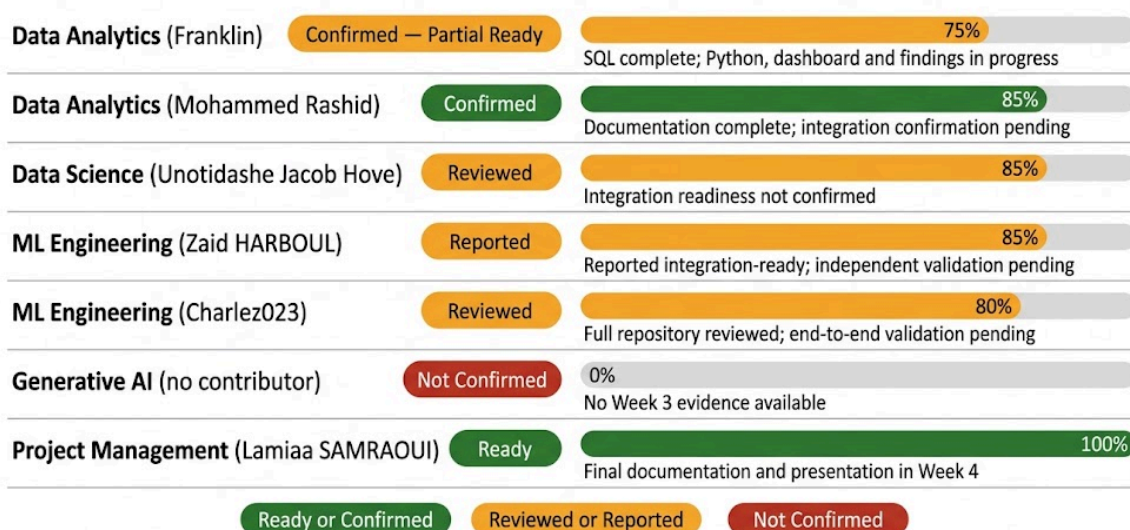


Figure 3: Integration Readiness Dashboard

Six-track readiness assessment with evidence-level badges. Only Project Management reaches “Ready” status. All cross-track items are Reported or Reviewed, not Confirmed.

Companion Excel Workbook

The Progress Review, Integration Readiness Tracker, Risk Register, Issue Log, Decision Log, and Week 4 Readiness Plan are also available as a single Excel workbook:

File: FinTrust_Week3_PM_Registers_Lamiaa_SAMRAOUI.xlsx

Location: Linked in the Google Drive submission folder

Sheets: Progress_Review, Integration_Readiness, Risk_Register, Issue_Log, Decision_Log, Week4_Readiness_Plan, Evidence_Sources

Section 4 — Updated Risk Register (Part C)

Risk Register Part 1 — Week 1 and 2 Risks with Week 3 Status

ID	Risk	Probability	Impact	Mitigation	Owner	Week 3 Status
----	------	-------------	--------	------------	-------	---------------



R-01	Data-quality issues	Medium	Medium	Data-profiling pass	DA and DS	Resolved
R-02	Track schedule slippage	Medium	High	Weekly tracking	PM	Changed
R-03	Dependency communication	Medium	Medium	Weekly register review	PM	Resolved
R-04	Predictive model limited by target imbalance	Medium	High	Realistic expectations documented	DS	Active
R-05	GenAI hallucination	Medium	High	No-invented-policy rule	GenAI	Active
R-06	Scope creep	Low	Medium	Reinforce governance	PM	Resolved
R-07	Tool access	Low	Medium	Confirm access	Individual and PM	Resolved
R-08	Limited buffer	Medium	High	Timeline milestones	PM	Active
R-09	Integration fails due to incompatible outputs	Medium	High	Flag format expectations	PM and MLE	Changed
R-10	Inconsistent documentation	Low	Medium	Share template	PM	Resolved
R-11	Unclear acceptance criteria	Medium	High	Define evidence early	PM	Changed
R-12	DA to DS hand-off timing	Medium	High	Confirm hand-off	PM	Resolved
R-13	GenAI grounding failures	High	High	Refine prompts and re-test	GenAI	Active

Risk Register Part 2 — New Risks Discovered in Week 3

ID	Risk	Probability	Impact	Rationale	Mitigation	Owner
----	------	-------------	--------	-----------	------------	-------

R-1 4	Week 4 time compression	High	High	Week 4 requires five activities (testing, refinement, documentation, integration, presentation) in one week. Any Week 3 slip cascades directly into Week 4.	Prioritise Week 4 critical path; complete documentation in advance; use Days 1 and 2 for validation only	PM
R-1 5	Cross-track integration readiness not confirmed	High	Medium	No track explicitly confirmed integration readiness in a form reviewable by the PM track. The Week 3 brief permits public-source use, but the limitation carries into Week 4.	Retain clear Reported and Reviewed labels; if formal collaboration begins in Week 4, request confirmation then	PM

Summary

Status	Count	Risk IDs
Resolved	6	R-01, R-03, R-06, R-07, R-10, R-12
Changed	3	R-02, R-09, R-11
Active	4	R-04, R-05, R-08, R-13
New	2	R-14, R-15
Total	15	All risks above

High-Priority Risks for Week 4

Rank	Risk	Why It Matters
1	R-13 (GenAI grounding)	Highest active risk; no Week 3 public evidence available
2	R-14 (Week 4 compression)	New risk; requires careful Week 4 planning

3	R-15 (Integration readiness not confirmed)	All cross-track statuses are Reported or Reviewed only
4	R-08 (Limited buffer)	Reinforced by R-14

Risk Heat Map

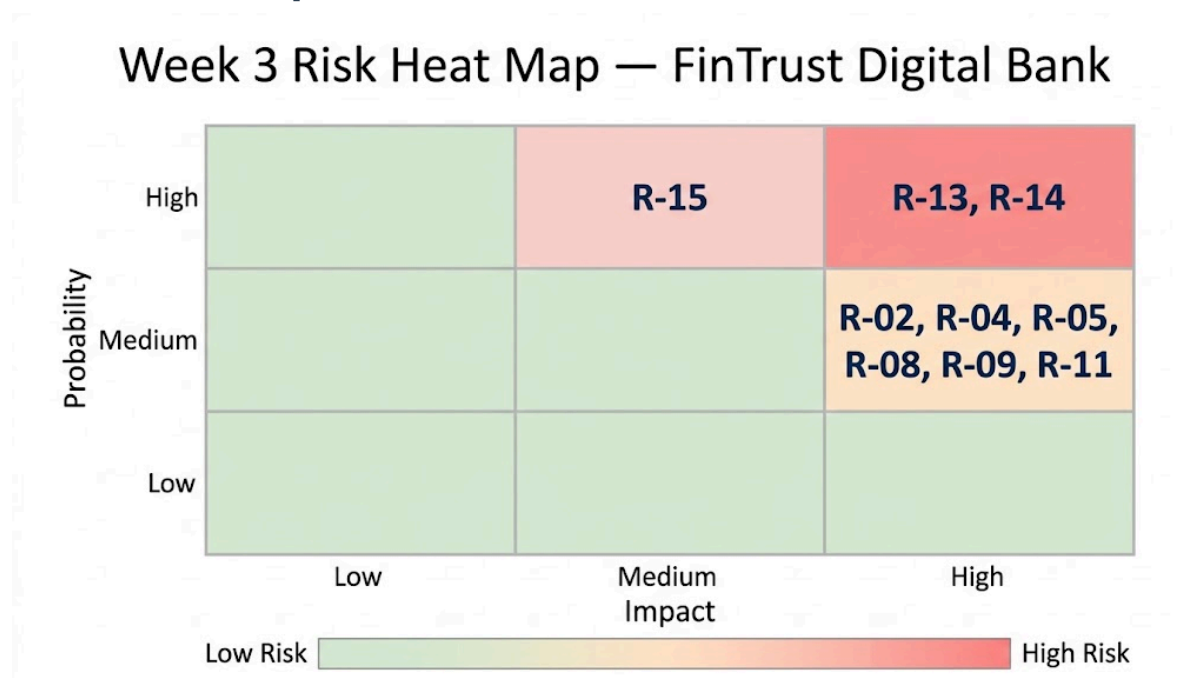


Figure 2: Week 3 Risk Heat Map

Nine open risks (of 15 tracked) plotted by probability and impact. R-13 and R-14 sit in the top-right quadrant. R-15 sits in the high-probability, medium-impact cell.

Interpretation

- Two risks (R-13 and R-14) sit in the high-probability, high-impact quadrant
- One risk (R-15) sits in the high-probability, medium-impact cell
- Six risks sit in the medium-probability, high-impact band
- Six risks were resolved in Week 3 and no longer appear on the heat map

Section 5 — Updated Issue Log (Part D)

Issue	Impact	Priority	Action	Owner	Status
-------	--------	----------	--------	-------	--------



Cross-track integration readiness not confirmed	Cannot fully validate integration until Week 4	High	Retain Reported and Reviewed labels; attempt confirmation in Week 4 if collaboration begins	PM	Open
Generative AI Week 3 evidence not available	R-13 status cannot be updated	Medium	Monitor for any new GenAI public update; note absence in Week 4	PM	Open
Two ML Engineering sources exist	Ambiguity about which source represents the final MLE output	Low	Document both sources; note relationship is not confirmed	PM	Open
No direct confirmation from any cross-track contributor	Integration readiness is provisional	High	Accepted as by-design for Week 3; attempt in Week 4	PM	Accepted
Resolved Week 1 risks still carried in register	Register was carrying stale items	Low	Marked Resolved and moved to resolved list	PM	Resolved
Week 3 timeline required new readiness column	Prior format insufficient for integration phase	Low	Added Integration Readiness Tracker with evidence levels	PM	Resolved

Legend:

- High Priority: needs immediate action
- Medium Priority: monitor and act in Week 4
- Low Priority: awareness only

Section 6 — Change and Decision Log (Part E)

Decision	Reason	Evidence	Impact	Date
----------	--------	----------	--------	------

Assessed four of five tracks as Reported or Reviewed complete based on public evidence	Public LinkedIn and GitHub sources available	Week 3 brief permits use of available outputs	Tracker updated with Reported and Reviewed statuses	Week 3, Day 1
Flagged Generative AI as Not Confirmed	No public Week 3 source found	Searches returned no GenAI Week 3 post	GenAI remains unconfirmed for Week 4	Week 3, Day 1
Adopted Reported and Reviewed framing instead of Confirmed and Validated	No cross-track source explicitly confirmed integration readiness	Review of all public sources	All cross-track statuses clearly labelled; no overstatement	Week 3, Day 2
Added R-14 (Week 4 time compression)	Week 4 brief requires five activities in one week	Week 4 roadmap	Week 4 Readiness Plan prioritises critical path	Week 3, Day 3
Added R-15 (Integration readiness not confirmed)	No track explicitly confirmed readiness	Review of all public sources	Risk register reflects honest evidence position	Week 3, Day 3
Used public LinkedIn and GitHub sources as evidence	No formal collaboration required; public sources available; no direct contact needed per Week 3 brief	Week 3 brief, "Important Week 3 Policy" section	Tracker updated; no overreach; no contact attempted	Week 3, Day 5
Did not attempt direct contact with cross-track contributors	Week 3 brief states individual responsibility; no collaboration expected	Week 3 brief	All cross-track evidence is public-source-only	Week 3, Day 5
Updated R-01, R-03, R-06, R-07, R-10, R-12 to Resolved	No further issues; statuses confirmed by Week 3 review	Risk review against Week 3 brief	Removes six risks from active tracking	Week 3, Day 4



Upgraded DA evidence level from “Reported” to “Reported Complete and Reviewed”	Additional DA documentation received beyond the LinkedIn post	Shared DA Week 3 documentation describing SQL, Python, dashboard and findings	DA tracker status updated; evidence level refined	Week 3, Day 5
--	---	---	---	---------------

Summary of Changes: Week 2 to Week 3

Type	Count	Details
Risks resolved	6	R-01, R-03, R-06, R-07, R-10, R-12
Risks changed	3	R-02, R-09, R-11
Risks still active	4	R-04, R-05, R-08, R-13
New risks	2	R-14, R-15
Total tracked	15	All risks listed in Section 4

Section 7 — Week 4 Readiness Plan (Part F)

The final week requires five activities to be completed in a single week. The plan below sequences them to protect the critical path.

Day	Activity	Priority	Owner	Dependencies
Day 1	Review any new public sources published after Week 3	Critical	PM	None
Day 1	If formal collaboration begins, request direct confirmation from available track members	Critical	PM	None
Day 1	Validate Week 3 assessments against any new information	Critical	PM	Day 1 actions above
Day 2	Final risk register update with Week 4 statuses	Critical	PM	Day 1 validation
Day 2	Final issue log update	Important	PM	Day 1 validation



Day 3	Complete Week 4 documentation	Critical	PM	All registers finalised
Day 3	Final timeline review and close-out	Important	PM	Day 2 updates
Day 4	Prepare presentation outline	Critical	PM	Day 3 documentation
Day 4	Draft 5 to 10 minute presentation	Important	PM	Day 4 outline
Day 5	Record presentation	Critical	PM	Day 4 draft
Day 5	Final submission to Drive	Critical	PM	Day 5 recording
Day 5	Update GitHub repository	Important	PM	Day 5 recording
Day 6 (buffer)	Any final revisions	Important	PM	All
Day 7 (deadline)	Final submission confirmation	Critical	PM	All

Critical Path: Review sources, Validate, Update registers, Complete documentation, Prepare presentation, Record, Submit

Risk Mitigation for R-14 (Week 4 compression):

- Documentation completed as much as possible before Day 3
- Presentation outline drafted before Day 4
- Days 1 and 2 focused on validation only
- Buffer day (Day 6) reserved for unforeseen issues

Section 8 — Week 3 Status Report

1. Overall Project Progress

The project is nearing completion. All PM deliverables for Week 3 are complete. Four of five tracks are Reported or Reviewed as complete based on public sources. One track (Generative AI) has no public Week 3 evidence available. The project is transitioning from development into final integration and preparation for presentation.

2. Activities Completed (PM Track)

- Week 3 Progress Review
- Integration Readiness Tracker with evidence levels
- Updated Risk Register (15 risks tracked)



- Updated Issue Log
- Change and Decision Log (Weeks 2 and 3)
- Week 4 Readiness Plan
- Week 3 Status Report
- Validation and Refinement Evidence
- Updated GitHub repository

3. Activities in Progress (Project-Wide, Assessed from Public Sources)

The following activities are based on public LinkedIn posts and GitHub repositories. They are not directly observed and no direct confirmation has been received:

- Data Analytics: Reported complete and reviewed (public LinkedIn post and shared DA documentation by Samuel Gichangi). Week 3 deliverables include advanced SQL analysis, expanded Python analysis with 5+ visualizations, a custom analytical dashboard, 5 validated business findings and 5 management recommendations. Integration readiness not explicitly stated.
- Data Science: Reported complete and repository reviewed (LinkedIn and GitHub by Unotidashe Jacob Hove). Integration readiness not confirmed.
- ML Engineering: Reported integration-ready by contributor (LinkedIn post by Zaid HARBOUL). Alternative repository reviewed (GitHub by Charlez023). Independent validation pending.
- Generative AI: No Week 3 public evidence available. Status not confirmed.

4. Delayed Activities

No delays identified in Week 3 based on public sources.

5. Major Risks

- R-13 (GenAI grounding) — Active, highest priority
- R-14 (Week 4 time compression) — Newly identified
- R-15 (Integration readiness not confirmed) — Newly identified
- R-08 (Limited buffer) — Active, reinforced by R-14

6. Major Issues

- Cross-track integration readiness not confirmed (High)
- Generative AI Week 3 evidence not available (Medium)
- Two ML Engineering sources exist (Low)

7. Decisions Made

Nine decisions logged in Section 6. Key decisions:

- Four of five tracks assessed as Reported or Reviewed complete



- Generative AI flagged as Not Confirmed
- Added R-14 and R-15
- Resolved six Week 1 and 2 risks
- Did not attempt direct contact with cross-track contributors

8. Project Health

At Risk

Rationale: Four of five tracks are Reported or Reviewed as complete, but no cross-track item reaches Confirmed or Validated level. Generative AI has no Week 3 public evidence. Week 4 compression (R-14) requires careful planning. New risk R-15 captures the integration-readiness gap. The project is trending toward On Track if Week 4 mitigations are executed as planned.

9. Recommended Week 4 Priorities

1. Confirm cross-track outputs where possible
2. Validate Week 3 assessments against any new information
3. Finalise risk register with Week 4 statuses
4. Complete Week 4 documentation
5. Prepare and record individual presentation
6. Final submission across all channels

Companion Status Deck

A short slide deck summarising the Week 3 status report is available:

File: FinTrust_Week3_PM_Status_Deck_Lamiaa_SAMRAOUI.pptx

Location: Linked in the Google Drive submission folder

Slides: 6 (Title, Integration Readiness, Risk Profile, Key Decisions, Week 4 Readiness Plan, Week 4 Priorities)

Section 9 — Validation and Refinement Evidence

This section demonstrates one meaningful improvement based on evidence, per the Week 3 brief.

Stage	Description
Initial Output	Week 2 Risk Register with 13 risks
Test	Reviewed against Week 3 brief requirements and available public sources; assessed each risk for current relevance



Finding	Six risks resolved (R-01, R-03, R-06, R-07, R-10, R-12); three risks changed status (R-02, R-09, R-11); two new risks identified (R-14 Week 4 compression; R-15 integration readiness not confirmed); DA Week 3 documentation received during Week 3, upgrading DA from “Reported” to “Reported Complete and Reviewed” evidence level
Refinement	Updated register with Week 3 statuses; added R-14 and R-15 with documented rationale; moved resolved risks to a resolved list; added Integration Readiness Tracker with evidence levels
Re-test	Reviewed updated register against Week 3 integration requirements; verified all active risks have mitigation actions and owners; verified all cross-track statuses are correctly labelled as Reported or Reviewed
Result	Risk Register now tracks 15 risks with honest evidence labels; Integration Readiness Tracker distinguishes Reported from Confirmed

Evidence of Improvement

- Week 2: Risk Register contained 13 risks, several of which no longer needed active tracking
- Week 3: Risk Register contains 15 risks, each with a current status and documented rationale
- Six risks formally resolved, two new risks added with rationale, four high-priority risks flagged for Week 4
- Integration Readiness Tracker now labels each track by evidence level

Section 10 — Week 1 and 2 Assumptions Status Update

Assumption	Week 3 Status
Weekly deadlines follow Sunday 11:59 PM WAT	Held
All five tracks staffed by individual interns	Held
Datasets and knowledge base available	Held
Tool access available for all tracks	Held
No formal collaboration required	Held
Weekly progress aligned with roadmap	Held



Section 11 — Limitations

- Cross-track integration readiness is assessed from public LinkedIn posts, GitHub repositories, and shared documentation. No direct communication with any cross-track contributor was made during Week 3, as the Week 3 brief confirms no formal collaboration is required.
- No cross-track status reaches Confirmed or Validated level. All statuses are Reported (public statement) or Reviewed (PM accessed public source).
- Two ML Engineering sources were found (Zaid HARBOUL LinkedIn post and Charlez023 GitHub repository); the relationship between them is not confirmed. Both are documented separately.
- No public Week 3 evidence was found for the Generative AI track.
- Data Analytics is now assessed at “Reported Complete and Reviewed” level, supported by a shared DA documentation file in addition to the LinkedIn post. Integration readiness remains not confirmed.
- Integration readiness may differ from reported completion. Confirming actual integration readiness will require Week 4 validation.
- All assessments will be validated against actual Week 4 outputs.

Section 12 — Conclusion

Week 3 has moved the FinTrust project from monitored execution into evidence-based integration readiness assessment. The PM track has completed all Week 3 deliverables, and the Integration Readiness Tracker now reflects publicly available and shared evidence from three of five cross-track tracks: Data Analytics (Samuel Gichangi — Reported Complete and Reviewed), Data Science (Unotidashe Jacob Hove — Reported Complete and Reviewed), and ML Engineering (Zaid HARBOUL — Reported Integration-Ready; Charlez023 — Reviewed Complete).

However, no cross-track source explicitly confirms integration readiness in a form reviewable by the PM track. The tracker therefore labels each status as Reported or Reviewed, never Confirmed or Validated. This distinction is deliberate: completed output is not the same as integration readiness.

The Week 3 brief confirms that individual responsibility is primary and that no formal cross-track collaboration is required. Public evidence was used where available. No direct contact with contributors was attempted. All cross-track statuses will remain provisional until Week 4 validation.

Project health remains At Risk, driven by the unconfirmed Generative AI readiness (R-13), the newly identified Week 4 time compression risk (R-14), and the newly added risk R-15 (integration readiness not confirmed).

The transition to final integration begins in Week 4. My focus will be on attempting direct confirmation of integration readiness if formal collaboration begins, validating the cross-track evidence, finalising all governance documents, and preparing the individual 5 to 10 minute presentation. The plan is intentionally prioritised to protect the critical path.



This Week 3 submission, along with Weeks 1 and 2, is maintained in my portfolio repository at <https://github.com/LamSa1/FinTrust-PM-Portfolio>.

