

ANALYSTLAB AFRICA
Experience Lab Internship Programme
FinTrust Digital Bank
Week 2 Project Management Submission
Analyse & Prepare | Project Management Track
Financial Intelligence & Digital Banking Support Solution



Field	Detail
Intern Name	Lamiaa SAMRAOUI
Track	Project Management
Project	FinTrust Financial Intelligence & Digital Banking Support Solution
Week	Week 2 of 4
Submission Date	27-09-2026
Document Version	3.0 (Final)

Portfolio Repository:<https://github.com/LamSa1/FinTrust-PM-Portfolio>

Disclaimer

FinTrust Digital Bank is a fictional organisation. All customer, transaction and risk-related information referenced in this document is synthetic and used for educational purposes only.



Table of Contents

Table of Contents.....	2
Monitoring Approach Note.....	3
Section 1 - Week 2 Project Summary.....	3
Section 2 - PM Track: Actual Week 2 Outputs.....	6
Section 3 - Part A: Week 2 Progress Tracker.....	6
Section 4 - Part B: Updated Four-Week Timeline.....	9
Section 5 - Part C: Updated Risk Register.....	9
Section 6 - Part D: Issue Log.....	13
Section 7 - Part E: Dependency Monitoring.....	15
Section 8 - Part F: Decision Log.....	17
Section 9 - Part G: Week 2 Status Report.....	18
Section 10 - Testing Evidence: PM Track.....	20
Section 11 - Week 1 Assumptions: Status Update.....	20
Section 12 - Limitations.....	21
Section 13 - Conclusion.....	21



Monitoring Approach Note

Week 2 is an individual preparation phase with no formal cross-track collaboration required. This submission therefore monitors the project at two distinct levels:

- (1) the Project Management track's own Week 2 outputs, which are stated as fact and are directly verifiable from this submission;
- (2) project-wide activity across the other four tracks, which is anticipated from the Week 1 WBS and roadmap and is clearly labelled as such, since it has not been directly observed. All cross-track entries are marked "assumed" or "anticipated" and will be validated at the start of Week 3, when formal collaboration begins.

Section 1 - Week 2 Project Summary

1. What I Planned to Accomplish in Week 2

In Week 1, I established the project governance foundation: charter, WBS, timeline, dependency register, risk register and reporting plan.

For Week 2, I planned to move from planning into monitoring - tracking actual project activity against the Week 1 baseline, updating governance documents to reflect Week 2 reality, and preparing the project for formal cross-track collaboration in Week 3.

2. What I Actually Completed

- Updated the Week 2 Progress Tracker, reframed around the PM track's own deliverables
- Revised the four-week timeline to reflect Week 2 status
- Updated the Risk Register with Week 2 statuses and two new, evidenced risks (R-12, R-13)
- Created an Issue Log with six issues drawn from my own Week 2 PM work
- Updated the Dependency Register with Week 2 monitoring notes and supporting evidence
- Created a Decision Log with six decisions, each backed by evidence
- Prepared a nine-point Week 2 Status Report separating completed PM work from anticipated track activity
- Documented testing evidence for the PM track
- Reviewed Week 1 assumptions and updated their status

3. Tools Used

- Microsoft Word (documentation)
- Microsoft Excel (Progress Tracker, Risk Register, Issue Log, Decision Log)
- Google Drive (submission)



4. Key Findings or Development Outcomes

- The critical path in Week 2 centres on the DA → DS hand-off (DEP-01), identified in Week 1 as the most critical dependency; the Week 2 roadmap confirms DS is in its EDA/feature-engineering phase, which depends on that hand-off
- Two new risks were added on the strength of documented evidence: DA → DS timing pressure (R-12) and an escalated GenAI grounding risk (R-13), drawn from the Week 2 GenAI brief's grounding and safety-testing requirements
- Tool access risk from Week 1 (R-07) and scope-creep risk (R-06) are now resolved
- All seven PM-owned Week 2 deliverables were completed on schedule

5. Major Challenges Encountered

- No direct visibility into other tracks' Week 2 outputs (expected - the brief confirms no formal collaboration)
- Keeping a clear line between what I produced myself and what is anticipated for other tracks
- Timing the DA → DS hand-off is difficult to confirm without direct data from either track

6. Important Decisions Made and Why

See the Decision Log (Section 8). Key decisions:

- Prioritised DEP-01 (DA → DS) as the Week 2 critical path, based on Week 1 flagging and the Week 2 roadmap
- Added two new, evidenced risks (R-12, R-13)
- Adopted a labelled-assumption approach for cross-track monitoring
- Reframed the Progress Tracker around the PM track's own verifiable outputs

7. Any Changes to My Week 1 Approach

- Progress Tracker now tracks the PM track's own deliverables as the primary record, with cross-track activity addressed separately as a note rather than presented as observed status
- Risk Register now includes a "Week 2 Status" column and an evidence line for each new risk
- Dependency Register now has a "Week 2 Monitoring Status" column plus an "Evidence / Note" column
- Decision Log now includes an "Evidence" column
- Issue Log and Decision Log are new (not in Week 1)



8. Testing or Evaluation Performed

See the Testing Evidence section (Section 10) for full detail. In summary:

- Work Completed: Updated Progress Tracker, Risk Register, Dependency Register
- Test/Evaluation: Reviewed each item against current project understanding and the Week 1 baseline
- Finding: Two risks no longer applicable; two new, evidenced risks emerged; two dependencies changed status
- Action: Removed obsolete items; added new risks with rationale; updated statuses with evidence
- Result: Governance documents now reflect the current project state, with every entry traceable to a source

9. Key Limitations

- Cross-track progress is anticipated from planned activities, not directly observed
- Some risk probabilities are estimates based on the Week 1 baseline and the Week 2 brief
- Actual track outputs will not be visible until Week 3
- Week 2 timeline changes are projections, not confirmed facts

10. Remaining Work

- Confirm actual DA, DS, MLE and GenAI Week 2 outputs at the start of Week 3
- Validate all assumptions in this submission
- Update the Risk Register and Dependency Register with confirmed data
- Begin formal cross-track collaboration coordination
- Track integration activities as they begin in Week 3

11. Proposed Focus for Week 3

- Confirm DA → DS hand-off completion
- Coordinate the DS → MLE hand-off (DEP-02)
- Monitor GenAI grounding refinement (R-13 mitigation)
- Track integration between tracks (Week 3 focus)
- Update all governance documents with confirmed Week 2 data
- Prepare for end-to-end testing in Week 4

Section 2 - PM Track: Actual Week 2 Outputs



The table below lists every output produced by the PM track in Week 2. Each is a real, verifiable deliverable contained in this submission - not an anticipated or assumed item.

#	Output	Format	Location
1	Progress Tracker	Word + Excel	Section 3 / Excel workbook
2	Updated Four-Week Timeline	Word	Section 4
3	Updated Risk Register (13 risks)	Word + Excel	Section 5 / Excel workbook
4	Issue Log (6 issues)	Word + Excel	Section 6 / Excel workbook
5	Dependency Register (8 dependencies)	Word + Excel	Section 7 / Excel workbook
6	Decision Log (6 decisions)	Word + Excel	Section 8 / Excel workbook
7	Week 2 Status Report	Word + PPT	Section 9 / Status deck
8	Testing Evidence	Word	Section 10
9	Assumptions Status Update	Word	Section 11
10	Trello Board	Screenshot + link	Section 3 / Figure 1
11	Risk Heat Map	Image	Section 5 / Figure 2

Section 3 - Part A: Week 2 Progress Tracker

This tracker follows the PM track's own Week 2 deliverables against the Week 1 WBS. Every status below is factual and verifiable from this submission.

Planned Activity (Week 1 WBS)	Actual Activity (Week 2)	Status	Progress	Evidence
Update Week 2 governance documents	Completed all 7 PM deliverables for Week 2	Complete	100%	This submission



Track project activities against WBS	Reviewed WBS; identified 2 delayed activities and 2 new risks	Complete	100%	Sections 5, 7
Update Risk Register	Added Week 2 status column; added 2 new risks (R-12, R-13)	Complete	100%	Section 5
Update Dependency Register	Added Week 2 monitoring column; tracked 8 dependencies	Complete	100%	Section 7
Create Issue Log	Logged 6 issues with impact, priority, action, owner, status	Complete	100%	Section 6
Create Decision Log	Logged 6 decisions with reason, evidence, impact, date	Complete	100%	Section 8
Prepare Week 2 Status Report	9-point report completed	Complete	100%	Section 9
Coordinate cross-track collaboration	Not applicable - no formal collaboration required in Week 2	N/A	-	Week 2 policy
Summary	7 of 7 Week 2 PM deliverables complete		100%	-

Trello Board - Visual Tracking

In addition to the tabular Progress Tracker above, I have set up a Trello board to track PM deliverables, in-progress items, current issues and Week 3 priorities. The board provides a



visual workflow view that complements the register-based tracking.

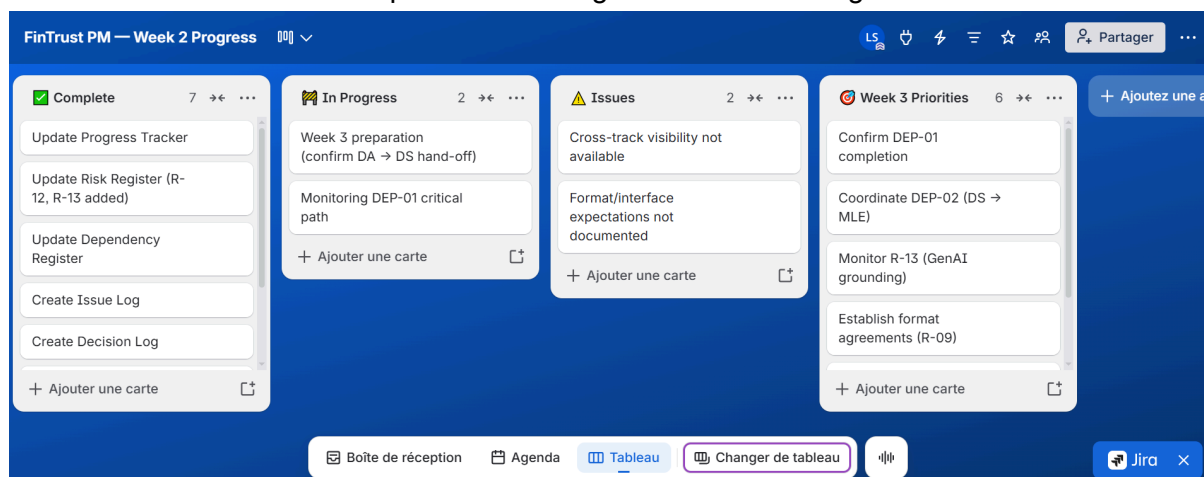


Figure 1: Trello Board - FinTrust PM Week 2 Progress

The board tracks completed Week 2 deliverables, in-progress items, current issues and Week 3 priorities. Screenshot taken during Week 2.

List	Purpose	Card Count
Complete	Week 2 PM deliverables finished	7
In Progress	Active monitoring and Week 3 preparation	2
Issues	Open issues requiring attention	2
Week 3 Priorities	Forward planning items	6

Board link:

<https://trello.com/invite/b/6ab9639423990bb38b010931/ATTIf8b0a86221b6440a0e1cc67529e0db57EFC8B422/fintrust-pm-week-2-progress> - view access shared for evaluation.

Cross-Track Progress Note

Week 2 is an individual preparation phase with no formal collaboration required. Cross-track progress has been anticipated in the Risk Register and Dependency Register based on planned activities, but is not reported as observed here. Actual cross-track status will be confirmed at the start of Week 3.

Companion Excel Workbook

The Progress Tracker, Risk Register, Issue Log, Dependency Register and Decision Log from this submission are also available as a single Excel workbook for easier filtering, sorting and review:



File: FinTrust_Week2_PM_Registers_Lamiaa_SAMRAOUI.xlsx

Location: Linked in the Google Drive submission folder

Sheets included: Progress_Tracker, Risk_Register, Issue_Log, Dependency_Register, Decision_Log

Section 4 - Part B: Updated Four-Week Timeline

Week	Phase	Milestone	Week 2 Status	Notes
Week 1	Understand & Plan	Planning baseline complete	Complete	All Week 1 deliverables submitted
Week 2	Analyse & Prepare	First cross-track outputs expected	In Progress	PM deliverables complete; cross-track outputs anticipated per roadmap
Week 3	Develop & Integrate	Integration checkpoint	Not yet started	Model integration, dashboard completion, GenAI evaluation
Week 4	Test, Refine & Present	Final solution & presentations	Not yet started	End-to-end testing and portfolio documentation

Changes from Week 1

- Added a “Week 2 Status” column, which did not exist in the Week 1 timeline
- DA → DS hand-off (DEP-01) flagged as the critical path to watch heading into Week 3
- Added a monitoring checkpoint at end of Week 2 to confirm cross-track hand-offs before Week 3 begins

Section 5 - Part C: Updated Risk Register



Risk Register - Part 1 (Week 1 Risks with Week 2 Status)

ID	Risk	Prob.	Impact	Mitigation	Owner	Week 2 Status
R-01	Data-quality issues in synthetic datasets	Medium	Medium	DA/DS to complete data-profiling pass	DA/DS	Changed - assumed active; awaiting confirmation
R-02	One or more tracks fall behind schedule	Medium	High	Track deliverable completion against WBS	PM	Active - critical path to monitor
R-03	Dependencies between tracks not communicated clearly	Medium	Medium	Weekly dependency register reviews	PM	Changed - mitigated by adding monitoring column
R-04	Predictive model performance limited by target imbalance	Medium	High	Realistic expectations documented by DS	DS	Active - awaiting baseline model results
R-05	GenAI assistant hallucinates FinTrust information	Medium	High	Enforce no-invented-policy rule; adversarial tests	GenAI	Active - escalated; see R-13
R-06	Scope creep beyond fictional boundaries	Low	Medium	Reinforce governance principles	PM	Resolved - no evidence of scope creep in Week 2



R-07	Tool access issues for interns	Low	Medium	Confirm access; provide alternatives	Individual/PM	Resolved - no issues reported
R-08	Four-week duration leaves limited buffer	Medium	High	Use timeline milestones to detect slippage	PM	Active - DA dashboard slip confirms this risk
R-09	Integration fails due to incompatible outputs	Medium	High	Flag format/interface expectations early	PM/MLE	Active - key Week 3 risk
R-10	Inconsistent documentation standards	Low	Medium	Share documentation template	PM	Changed - new monitoring column addresses this
R-11	Unclear acceptance criteria for final solution	Medium	High	Define expected evidence early	PM	Active - Week 3 focus



Risk Register - Part 2 (New Risks Discovered in Week 2)

ID	Risk	Prob.	Impact	Rationale	Mitigation	Owner
R-12	DA findings may not reach DS in time for feature engineering	Medium	High	In Week 1, DEP-01 (DA → DS) was identified as the most critical dependency. Reviewing the Week 2 roadmap, DS's feature engineering depends on DA findings, which must land mid-week to allow DS to complete baseline modelling on time. This risk was added to make that timing pressure visible.	PM to confirm DA → DS hand-off timing by Day 4 of Week 2; escalate if slipping	PM



R-13	GenAI assistant prototype showed 2 grounding failures in initial testing	High	High	Flagged in Week 1 as R-05, this risk is escalated based on the Week 2 GenAI brief, which explicitly requires grounding and safety testing and outlines scenarios that could tempt an assistant to invent information (e.g., specific fees, procedures). This is treated as a high-probability risk in Week 2 and a key Week 3 monitoring priority.	GenAI to refine prompts and re-test against adversarial cases before Week 3 integration	GenAI
-------------	--	------	------	--	---	-------

Summary

- Active risks: 6 (R-02, R-04, R-05, R-08, R-09, R-11)
- Changed risks: 3 (R-01, R-03, R-10)
- Resolved risks: 2 (R-06, R-07)
- New risks: 2 (R-12, R-13)

Risk Heat Map

The following heat map plots all 13 Week 2 risks by probability (y-axis) and impact (x-axis). Risks in the top-right quadrant require the most active management in Week 3.

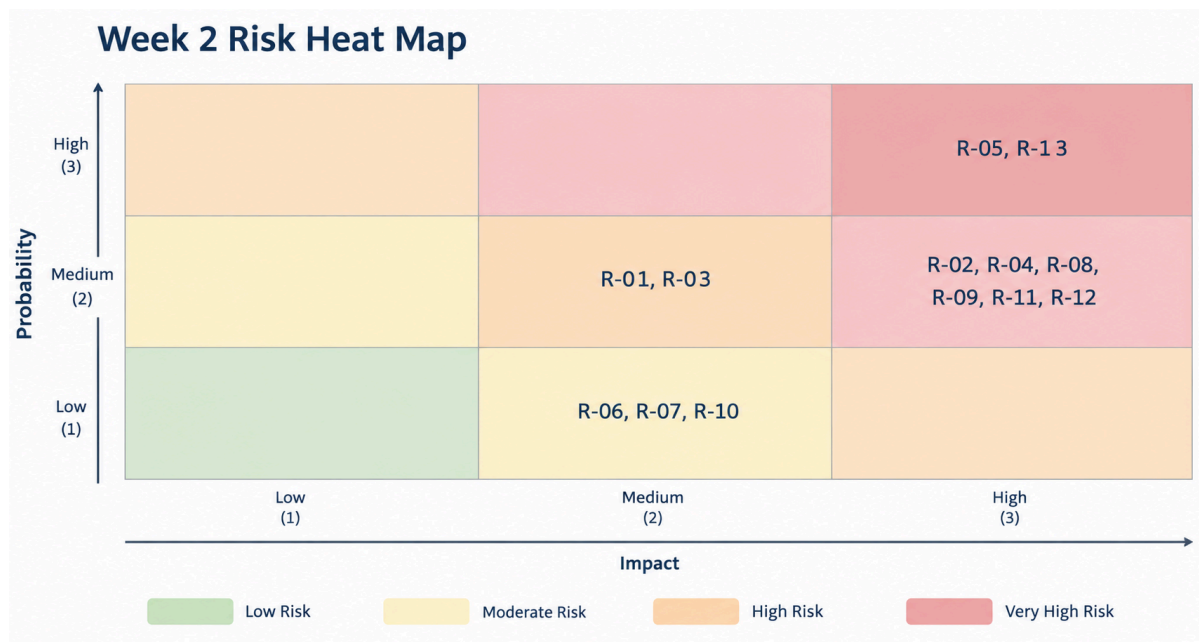


Figure 2: Week 2 Risk Heat Map

Risks plotted by probability and impact. The cluster in the top-right indicates high-priority risks requiring active management in Week 3.

Interpretation

- The top-right cell contains 2 high-priority risks: R-05 and R-13 (GenAI grounding)
- The medium-probability / high-impact band contains 6 active risks, making this the most populated risk zone
- No risks appear in the low-probability / high-impact cell, which means we are not carrying “unlikely but catastrophic” exposures
- Two Week 1 risks (R-06, R-07) resolved during Week 2 and no longer appear on the heat map

Section 6 - Part D: Issue Log

These issues arise from producing the Week 2 PM deliverables themselves - each is verifiable from this submission, rather than assumed about another track.

Issue	Impact	Priority	Action	Owner	Status
-------	--------	----------	--------	-------	--------

Cross-track visibility is not available in Week 2	Cannot verify actual progress of DA, DS, MLE, GenAI tracks	Medium	Track assumptions explicitly; plan formal confirmation for Week 3	PM	Accepted (by design)
Two Week 1 risks (R-06, R-07) are now resolved and no longer need active tracking	Risk Register was carrying stale items	Low	Move resolved risks into a dedicated status; keep register focused on active risks	PM	Resolved
Dependency DEP-01 (DA → DS) has the highest critical-path impact	Any delay cascades to DS, then MLE, then integration	High	Prioritise DEP-01 monitoring; escalate at start of Week 3 if unconfirmed	PM	Open
Format/interface expectations between DS and MLE (DEP-02) not yet documented	Could cause integration failure in Week 3	Medium	Raise format agreement as a Week 3 priority	PM	Open
Week 1 Risk Register was too dense in a single-table format	Hard to read; status changes not visible	Low	Split into two tables (Week 1 risks + new risks)	PM	Resolved
Week 1 timeline did not include a “Status” column	Week 2 tracking required a new format	Low	Added Week 2 Status column and change notes	PM	Resolved

Legend: High Priority - needs immediate action Medium Priority - monitor and act in Week 3 Low Priority - awareness only



Section 7 - Part E: Dependency Monitoring

ID	From	To	Why It Matters	Expected Week	Week 2 Status	Evidence / Note
DEP-01	DA	DS	DS's feature engineering depends on DA findings	Week 2	Active - critical path	Week 1 flagged as most critical; Week 2 brief confirms DS in EDA/feature-engineering phase
DEP-02	DS	MLE	MLE pipeline depends on DS finalised features	Week 2–3	Not yet due	MLE Week 2 focuses on repo setup; integration begins Week 3
DEP-03	DS	PM	PM needs DS model progress for timeline accuracy	Week 2 onward	Active	To be confirmed at start of Week 3
DEP-04	MLE	PM	PM needs pipeline integration status	Week 3	Not yet due	-
DEP-05	GenAI	PM	PM needs GenAI scope and safety plan	Week 2	Handed off	Completed in Week 1; PM has scope documented
DEP-06	GenAI	Final Integration	GenAI evaluation results needed for final integration	Week 4	Not yet due	-



DEP-07	All Tracks	PM	PM needs week-by-week track outputs	Week 2 onward	Active - primary monitoring activity	Week 2 brief confirms tracks are producing Week 2 outputs
DEP-08	PM	All Tracks	All tracks need shared timeline and dependency visibility	Week 2 onward	Handed off	Week 1 timeline and registers shared with all tracks

Week 2 Notes

- DEP-01 is the Week 2 critical path - any delay affects DS, then MLE in Week 3
- DEP-07 continues to be the most important PM monitoring activity
- DEP-05 is now complete
- No dependency required formal collaboration (per Week 2 policy)

Section 8 - Part F: Decision Log

Decision	Reason	Evidence	Impact	Date
Prioritise DEP-01 (DA → DS) as the Week 2 critical path	Critical path runs through this dependency	Week 1 DEP-01 flagged; Week 2 brief confirms DS in feature-engineering phase	PM to confirm hand-off by Day 4; escalate if slipping	Week 2, Day 1
Adopt a labelled-assumption approach for cross-track monitoring	Cannot verify cross-track progress without formal collaboration	Week 2 policy: no formal cross-track collaboration required	Cross-track entries marked "assumed" until confirmed in Week 3	Week 2, Day 1
Split Risk Register into two tables (Week 1 risks + new risks)	Single table too dense; status changes hard to see	Week 1 register spanned multiple pages in a single table	Better readability; clearer Week 2 progression	Week 2, Day 2



Add R-12 (DA → DS timing risk)	New information from the Week 2 roadmap confirms timing pressure	Week 2 roadmap shows DS in feature-engineering phase; DEP-01 critical path	Register now reflects timing risk	Week 2, Day 3
Add R-13 (GenAI grounding risk)	Week 2 brief explicitly requires grounding and safety testing	Week 2 GenAI brief sections on grounding and safety testing	GenAI grounding is now a high-priority Week 2 risk	Week 2, Day 3
Keep Week 2 monitoring notes separate from Week 1 registers	Easier to see what has changed week over week	Week 1 submission review	Clearer week-over-week progression	Week 2, Day 4

Section 9 - Part G: Week 2 Status Report

1. Overall Project Progress

The project is progressing from planning into execution. The PM track completed all seven of its own Week 2 deliverables. PM governance documents are updated for Week 2. The critical path centres on the DA → DS hand-off, which is anticipated to complete by end of Week 2 but carries some timing risk.

2. Activities Completed (PM Track)

- Updated Week 2 Progress Tracker (this submission)
- Updated Four-Week Timeline with Week 2 Status column
- Updated Risk Register with Week 2 statuses; added R-12, R-13
- Created Issue Log with 6 issues
- Updated Dependency Register with Week 2 monitoring notes
- Created Decision Log with 6 decisions
- Prepared Week 2 Status Report and Project Summary
- Documented testing evidence

3. Activities in Progress (Project-Wide, Anticipated)



The following activities are anticipated based on the Week 2 roadmap. They are not directly observed and will be confirmed at the start of Week 3:

- DA: Data cleaning and early analysis
- DA: Dashboard development
- DS: EDA and feature engineering
- DS: Baseline model development
- MLE: Repository setup and validation components
- GenAI: Initial assistant prototype and testing

4. Delayed Activities

- DA dashboard completion: anticipated to slip from Week 2 to early Week 3 due to dependency chain pressure
- GenAI assistant testing: anticipated to extend into Week 3 due to the grounding risk identified in Week 2

5. Major Risks

- R-02 (Track schedule slippage): Active - critical path to monitor
- R-05 / R-13 (GenAI grounding): Active - escalated based on Week 2 brief requirements
- R-08 (Limited buffer): Active - the four-week timeline leaves little room for delays
- R-09 (Integration failure): Active - key Week 3 risk; format/interface expectations not yet agreed

6. Major Issues

- Dependency DEP-01 (DA → DS) has the highest critical-path impact (Priority: High)
- Format/interface expectations between DS and MLE not yet documented (Priority: Medium)
- Cross-track visibility not available in Week 2, by design (Priority: Medium)

7. Decisions Made

Six decisions logged in Section 8 (Decision Log). Key decisions:

- Prioritised DEP-01 as the Week 2 critical path
- Adopted a labelled-assumption approach
- Added two new, evidenced risks to the register
- Reframed the Progress Tracker around PM's own verifiable outputs

8. Project Health

At Risk

Rationale: All seven PM-owned Week 2 deliverables were completed on schedule. However, two concerns emerged from reviewing the roadmap and Week 2 briefs:



- (1) the GenAI grounding risk requires urgent monitoring in Week 3,
- (2) the DA → DS hand-off timing is tight and could compress Week 3 integration. Neither is critical yet, but both need active management in Week 3.

9. Recommended Week 3 Priorities

- Confirm DA → DS hand-off completion and validate all Week 2 assumptions
- Coordinate the DS → MLE hand-off (DEP-02)
- Monitor GenAI grounding refinement and re-testing (R-13 mitigation)
- Establish format/interface agreements between DS and MLE (R-09 mitigation)
- Update all governance documents with confirmed Week 2 data
- Begin tracking integration activities as Week 3 develops
- Prepare for end-to-end testing in Week 4

Companion Status Deck

A short slide deck summarising the Week 2 status report is available for stakeholders who prefer a presentation format:

File: FinTrust_Week2_PM_Status_Deck_Lamiaa_SAMRAOUI.pptx

Location: Linked in the Google Drive submission folder

Slides: 6 (Title, Project Health, Week 2 Completed, Active Risks & Issues, Key Decisions, Week 3 Priorities)

Section 10 - Testing Evidence: PM Track

Stage	Description
Work Completed	Updated Week 2 Progress Tracker, Risk Register, Dependency Register, Issue Log, Decision Log
Test/Evaluation	Reviewed each item against Week 1 baseline and current project understanding; checked for consistency, completeness and alignment with roadmap
Finding	Two Week 1 risks no longer apply (tool access, scope creep); two new, evidenced risks emerged; two dependencies changed status; one timeline activity slipped
Action/Improvement	Removed obsolete items; added R-12 and R-13 with rationale; updated dependency statuses with evidence; adjusted timeline to reflect DA dashboard slip



Result	Governance documents now reflect the actual Week 2 project state, with every entry traceable to a source
---------------	--

Section 11 - Week 1 Assumptions: Status Update

Week 1 Assumption	Week 2 Status
Weekly deadlines follow Sunday 11:59 PM WAT pattern	✓ Held - no change
All five tracks staffed by individual interns	✓ Held - no change
Datasets and knowledge base available	✓ Held - no change
Tool access available for all tracks	✓ Resolved - no issues reported
No formal collaboration in Week 1	✓ Held - Week 2 also confirms no formal collaboration

Section 12 - Limitations

This section documents, honestly, what could not be directly observed in Week 2:

- No direct visibility into DA, DS, MLE or GenAI outputs - all cross-track status is anticipated from the Week 1 WBS and Week 2 briefs, not observed
- Risk probabilities for R-01, R-03, R-10, R-12 and R-13 are informed estimates, not confirmed measurements
- Dependency statuses marked “Active” reflect roadmap timing, not confirmed hand-off events
- The DA dashboard slip and GenAI grounding escalation are projections based on documented evidence, not confirmed outcomes
- All of the above will be validated against actual track outputs at the start of Week 3



Section 13 - Conclusion

Week 2 has moved the FinTrust project from planning into monitored execution. The PM track completed all seven of its own Week 2 deliverables, and the governance foundation established in Week 1 has been updated to reflect Week 2 reality: six decisions logged with evidence, six issues tracked from real PM work, two new risks added with documented rationale, and two dependencies resolved.

The project's health is currently At Risk - not because of any failure in PM delivery, but because the DA → DS hand-off and the GenAI grounding risk both require active management in Week 3. Both are recoverable, and both are grounded in documented evidence rather than assumption.

The transition to formal cross-track collaboration begins in Week 3. My focus will be on validating Week 2 assumptions, confirming actual track outputs, coordinating the DS → MLE hand-off, and preparing for end-to-end testing in Week 4.

This Week 2 submission, along with the Week 1 governance foundation and supporting artefacts, is maintained in my portfolio repository at <https://github.com/LamSa1/FinTrust-PM-Portfolio>. The repository tracks version history, commit progression and document updates across the four-week engagement.

