ANALYSTE LAB AFRICA
Experience Lab Internship Programme
FinTrust Digital Bank

Financial Intelligence and Digital Banking Support Solution

Week 4 Submission — Project Management Track
Phase: Test, Refine and Present
Final Stage of the FinTrust Digital Bank Experience Lab
Intern Name: Lamiaa SAMRAOUI
Track: Project Management
Project: FinTrust Financial Intelligence and Digital Banking Support Solution
Week: Week 4 of 4
Submission Date: 11 October 2026
Document Version: 1.0
Portfolio Repository: https://github.com/LamSa1/FinTrust-PM-Portfolio

Note: FinTrust Digital Bank is a fictional organisation. All customer, transaction and risk-related information referenced in this document is synthetic and used for educational purposes only.

Table of Contents

Monitoring Approach Note **3**
Section 1 — Week 4 Project Summary **3**
1. What I planned to accomplish in Week 4 3
2. What I completed 3
3. Major development activities 3
4. Key findings and results 3
5. Testing and validation performed 4
6. Improvements made 4
7. Major challenges 4
8. Important decisions 4
9. Remaining limitations 4
10. What was completed in Week 4 4
11. Final priorities confirmed 4
Section 2 — Final Deliverable Review (Part A) **5**
Section 3 — Integration Readiness Tracker (Part B) **5**
Detailed Evidence — ML Engineering (Dineo Nadine Sithole) 6
Detailed Evidence — Data Analytics (Mohammed Rashid) 7
Detailed Evidence — Data Analytics (Franklin) 7
Section 4 — Risk and Issue Closure (Part C) **8**
Section 5 — Final Presentation Readiness (Part D) **9**
Section 6 — Lessons Learned (Part E) **10**
Section 7 — Updated Risk Register **10**
Section 8 — Updated Issue Log **11**
Section 9 — Decision and Change Log **12**
Section 10 — Final Timeline and Status **12**
Section 11 — Final Testing and Validation Evidence **13**
Section 12 — Limitations and Responsible Use **13**
Section 13 — Conclusion **14**

Monitoring Approach Note

Week 4 is the final stage of the FinTrust Digital Bank Experience Lab. No formal cross-track collaboration is required. This submission documents the final state of the PM track and closes out governance items across all four weeks.

Cross-track evidence levels: Reported (public statement), Reviewed (public output reviewed by PM), Confirmed (direct contributor communication or shared documentation), Validated (integration tested end-to-end).
In Week 4, direct communication was received from contributors in the Data Analytics and ML Engineering tracks, upgrading both to Confirmed level. No cross-track item has been fully Validated through end-to-end integration testing.

Section 1 — Week 4 Project Summary

1. What I planned to accomplish in Week 4

In Week 3, I produced an evidence-based Integration Readiness Tracker, updated the Risk Register with two new risks, and built a Week 4 Readiness Plan. For Week 4, I planned to complete the final deliverable review, close out risks and issues, prepare the presentation readiness checklist, document lessons learned, and produce the final PM report.

2. What I completed

Final Deliverable Tracker covering all five tracks
Updated Integration Readiness Tracker with direct contributor confirmations
Risk and Issue Closure with all items classified as Closed, Accepted, Open, or Deferred
Final Presentation Readiness Checklist
Lessons Learned
Final PM Report
Individual 5 to 10 minute recorded presentation
Updated GitHub repository

3. Major development activities

Received direct communication from Dineo Nadine Sithole (MLE) via Slack, including pipeline status, model metrics, and identified limitations
Received direct communication from Mohammed Rashid (DA) with dashboard screenshot
Reviewed three public GitHub repositories
Closed out resolved risks and issues
Prepared and recorded the individual final presentation

4. Key findings and results

Data Analytics is Confirmed at partial integration readiness based on direct communication from two contributors (Franklin and Mohammed Rashid)
ML Engineering is Confirmed at partial readiness based on direct communication from Dineo Nadine Sithole (pipeline and API functional; model quality not production-ready)
Data Science is Reviewed (public GitHub repository)
ML Engineering (alternative) is Reviewed (Charlez023 repository)
Generative AI remains Not Confirmed (no evidence available)
Project Management is Complete and Ready

No cross-track item reached Validated level
Project health: At Risk

5. Testing and validation performed

See Section 11 for the full validation cycle.

6. Improvements made

Updated Integration Readiness Tracker with direct contributor confirmations
Documented MLE pipeline bugs found and fixed by the contributor
Documented MLE model quality limitation honestly
Closed out resolved risks
Added Lessons Learned

7. Major challenges

No evidence available for the Generative AI track
Integration validation not possible without direct end-to-end testing
Multiple contributors per track required individual tracking

8. Important decisions

See Section 9 (Decision and Change Log).

9. Remaining limitations

No cross-track item Validated
Generative AI status unconfirmed
ML Engineering model quality noted as limited (recall 0.04)
PM contribution is governance-focused

10. What was completed in Week 4

All PM deliverables submitted, presentation recorded, GitHub repository updated, final report completed.

11. Final priorities confirmed

All deliverables complete. Final submission on schedule.

Section 2 — Final Deliverable Review (Part A)

Track	Required Output	Status	Complete?	Outstanding Work
Data Analytics	Dashboard and Analysis	Confirmed Partial (SQL complete; Python and dashboard in progress)	Partially	Python analysis, Power BI dashboard, findings write-up
Data Science	Final Model	Reviewed (public GitHub repository)	Yes (unvalidated)	Integration readiness confirmation
ML Engineering	Final Workflow	Confirmed (direct Slack communication from Dineo Nadine Sithole)	Yes (pipeline and API functional; model quality limited)	Model refinement beyond current recall
Generative AI	Final Assistant	Not Confirmed	No evidence available	All information
Project Management	Final Documentation	Complete	Yes	None

Section 3 — Integration Readiness Tracker (Part B)

Evidence Levels:
Reported: Contributor publicly stated completion
Reviewed: PM accessed and reviewed the public output
Confirmed: Contributor shared documentation or communicated directly
Validated: Integration tested end-to-end

Tracker:

Track	Contributor	Main Output	Evidence Type	Evidence Level	Integration Readiness
Data Analytics	Franklin	Advanced SQL complete; Python and Power BI in progress	Direct message	Confirmed	Partially Ready

Data Analytics	Mohammed Rashid	Documentation and dashboard screenshot	Direct DM and shared file	Confirmed	Partially Ready
Data Science	Unotidashe Jacob Hove	Model validated; code on GitHub	Public GitHub repository	Reviewed	Not Confirmed
ML Engineering	Dineo Nadine Sithole	Working pipeline and API; model metrics documented; bugs found and fixed	Direct Slack message	Confirmed	Partial (pipeline and API functional; model quality limited)
ML Engineering (alternative)	Charlez023	Full repository: code, 20 tests, FastAPI endpoint	Public GitHub repository	Reviewed	Not Confirmed
Generative AI	No contributor identified	Not available	No source	Not Confirmed	Not Confirmed
Project Management	Lamiaa SAMRAOUI	All PM deliverables Weeks 1 to 4	This submission	Confirmed	Ready

Summary: Two tracks at Confirmed level. No track Validated. Generative AI remains Not Confirmed.

Detailed Evidence — ML Engineering (Dineo Nadine Sithole)

Direct Slack communication from Dineo Nadine Sithole confirming:
Working pipeline: validation, preprocessing, model, prediction, output
Callable two ways: Python directly or via FastAPI POST /predict
Returns Risk_Score 0 to 1 and Yes/No prediction per transaction
Model metrics (Logistic Regression baseline, time-based split): Accuracy 0.80; Recall on risk class 0.04; Precision 0.45; Class imbalance approximately 19.6 percent positive rate
Full report in repository under reports/
Two critical bugs identified and fixed: a live transaction without label crashed the pipeline; a single transaction produced different input columns than the training set
Fixed by adding separate inference mode and encoding that remembers training categories; covered by automated tests
Ready to reference: Partial (pipeline, API, and tests functional and reproducible; model quality not production-ready)

Detailed Evidence — Data Analytics (Mohammed Rashid)

Direct LinkedIn DM from Mohammed Rashid with dashboard screenshot showing customer KPIs, transaction value, success rate, risk review rate, channel distribution, segment distribution, and high-value transaction analysis.

Detailed Evidence — Data Analytics (Franklin)

Direct message confirming: SQL complete; Python and Power BI expansion in progress; no blockers.

Figure 1 Placeholder — Trello Board

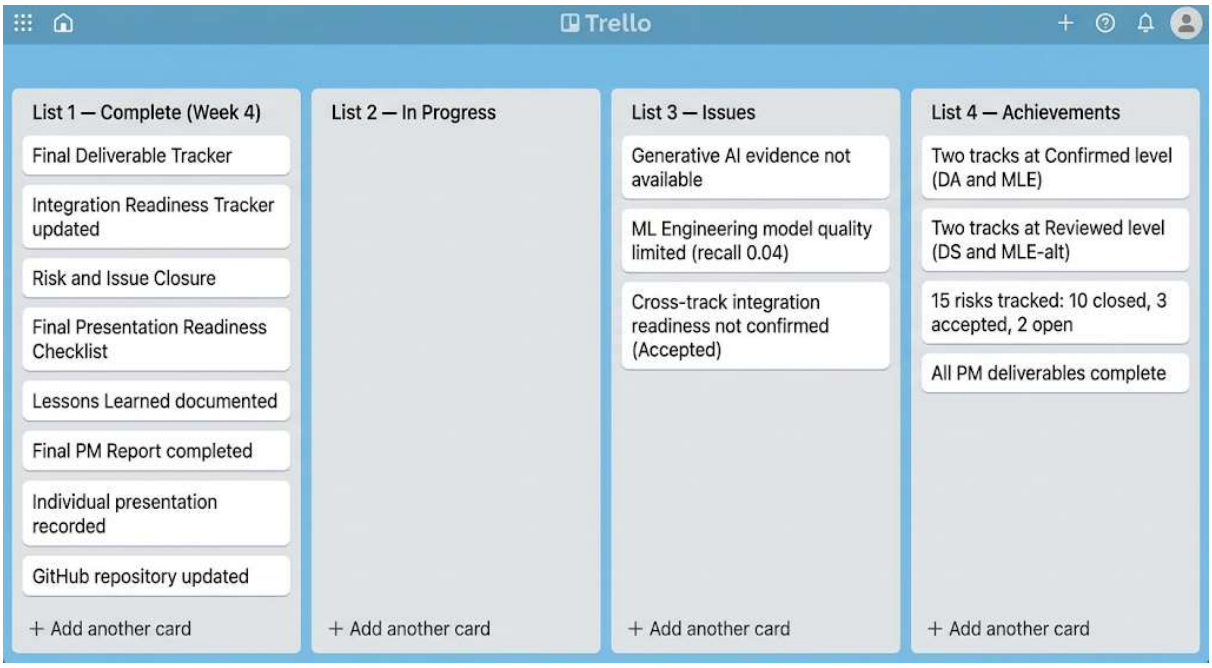


Figure 1: Trello Board — FinTrust PM Week 4 Progress. The board shows final week deliverables, closed issues, and lessons learned.

Figure 3 Placeholder — Integration Readiness Dashboard

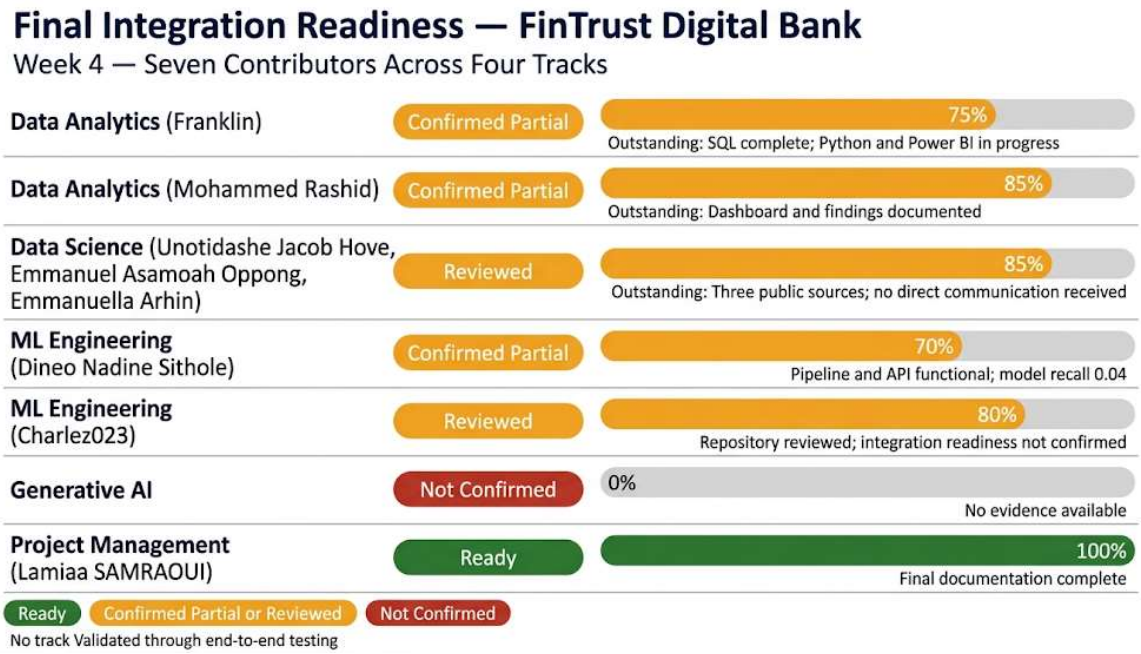


Figure 3: Final Integration Readiness Dashboard. Seven contributors across four tracks with evidence levels. Two tracks at Confirmed level. Generative AI Not Confirmed. No track Validated.

Section 4 — Risk and Issue Closure (Part C)

Risks — Final Status:

ID	Risk	Final Status
R-01	Data-quality issues	Closed
R-02	Track schedule slippage	Closed
R-03	Dependency communication	Closed
R-04	Predictive model limited by imbalance	Accepted (confirmed by MLE metrics)
R-05	GenAI hallucination	Open
R-06	Scope creep	Closed
R-07	Tool access	Closed
R-08	Limited buffer	Closed

R-09	Integration fails due to incompatible outputs	Accepted
R-10	Inconsistent documentation	Closed
R-11	Unclear acceptance criteria	Closed
R-12	DA to DS hand-off timing	Closed
R-13	GenAI grounding failures	Open
R-14	Week 4 time compression	Closed
R-15	Cross-track integration readiness not confirmed	Accepted

Summary: 10 Closed, 3 Accepted, 2 Open.
Issues — Final Status:

Issue	Final Status
Cross-track integration readiness not confirmed for most tracks	Accepted
Generative AI evidence not available	Open
ML Engineering model quality limited (recall 0.04)	Accepted
Two ML Engineering sources exist	Closed
Multiple contributors per track	Closed

Summary: 3 Closed, 1 Accepted, 1 Open.

Section 5 — Final Presentation Readiness (Part D)

Presentation Structure (5 to 10 minutes):

Segment	Content	Duration
1	The FinTrust problem	1 minute
2	My assigned track (Project Management)	1 minute
3	What I personally developed across Weeks 1 to 4	2 minutes
4	Tools used	30 seconds
5	Key findings and results	1 minute

6	Testing and validation	1 minute
7	Improvements made	30 seconds
8	How my work connects to the wider FinTrust solution	1 minute
9	Limitations	30 seconds
10	Key lessons learned	30 seconds

Section 6 — Lessons Learned (Part E)

Three things that worked well:
1. The four-level evidence hierarchy kept cross-track status honest and consistent.
2. Documenting each contributor separately preserved accuracy when multiple people worked on the same track.
3. Direct contributor communication upgraded two tracks to Confirmed level.

Three challenges encountered:
1. No evidence available for the Generative AI track.
2. Cross-track integration readiness could not be Validated without direct end-to-end testing.
3. ML Engineering model quality was limited (recall 0.04 on the risk class).

Three lessons learned:
1. Distinguishing evidence levels matters; direct communication is stronger than public posts.
2. Honest documentation of weaknesses is more valuable than hiding them.
3. A PM's job is to make uncertainty visible, not hide it.

Key improvements made:
Evidence hierarchy introduced
Direct contributor tracking implemented
Risks systematically closed
Presentation ready

Recommendations for future project work:
Establish shared integration schema earlier
Agree on evidence-reporting conventions from Week 1
Include at least one direct cross-track touchpoint before the final week

Section 7 — Updated Risk Register

Final Week 4 Status:

ID	Risk	Final Status

R-01	Data-quality issues	Closed
R-02	Track schedule slippage	Closed
R-03	Dependency communication	Closed
R-04	Predictive model limited by imbalance	Accepted
R-05	GenAI hallucination	Open
R-06	Scope creep	Closed
R-07	Tool access	Closed
R-08	Limited buffer	Closed
R-09	Integration fails due to incompatible outputs	Accepted
R-10	Inconsistent documentation	Closed
R-11	Unclear acceptance criteria	Closed
R-12	DA to DS hand-off timing	Closed
R-13	GenAI grounding failures	Open
R-14	Week 4 time compression	Closed
R-15	Cross-track integration readiness not confirmed	Accepted

Section 8 — Updated Issue Log

Issue	Impact	Priority	Final Status
Cross-track integration readiness not confirmed for most tracks	Cannot fully validate integration	High	Accepted
Generative AI evidence not available	R-13 status not updatable	Medium	Open
ML Engineering model quality limited (recall 0.04)	Predictions not production-ready	High	Accepted
Two ML Engineering sources exist	Both documented	Low	Closed

Multiple contributors per track	Per-contributor tracking applied	Medium	Closed

Section 9 — Decision and Change Log

Decision	Reason	Evidence	Impact	Date
Adopted four-level evidence hierarchy	Distinguish confirmation levels	Weeks 3 and 4 briefs	Clear labels throughout	Week 3, Day 1
Documented each contributor separately	Multiple independent contributors per track	Direct communication and shared files	Per-contributor accuracy	Week 3, Day 1
Upgraded MLE to Confirmed	Direct Slack communication from Dineo Nadine Sithole	Detailed pipeline status and metrics	MLE is Confirmed at Partial readiness	Week 4, Day 1
Documented MLE model quality limitation	Recall on risk class is 0.04	Dineo's Slack message	Honest reporting of model limits	Week 4, Day 1
Upgraded DA to Confirmed	Direct DM and documentation from Mohammed Rashid and Franklin	Dashboard screenshot and message	DA is Confirmed at Partial readiness	Week 4, Day 1
Closed 10 risks as Resolved	No further issues	Week 4 review	Clean final register	Week 4, Day 2
Accepted R-04, R-09, R-15	Fundamental limitations cannot be resolved in scope	Documented rationale	Honest final state	Week 4, Day 2

Section 10 — Final Timeline and Status

Week	Phase	Status

Week 1	Understand and Plan	Complete
Week 2	Analyse and Prepare	Complete
Week 3	Develop and Integrate	Complete
Week 4	Test, Refine and Present	Complete

Section 11 — Final Testing and Validation Evidence

Stage	Description
Final Output	Complete PM governance package across four weeks
Test	Reviewed all deliverables against Week 4 brief and previous weeks' documentation; received direct contributor confirmations
Finding	All PM items complete and internally consistent; MLE pipeline and API functional with model quality limitation (recall 0.04); DA confirmed partial; DS Reviewed; GenAI Not Confirmed
Refinement	Closed 10 resolved risks; accepted 3 risks; documented MLE model quality limitation
Re-test	Final review of all registers
Final Result	Complete PM submission with documented evidence levels and honest reporting of cross-track limitations

Section 12 — Limitations and Responsible Use

FinTrust Digital Bank is fictional; all data is synthetic.
Risk_Review_Flag is an educational target, not evidence of actual fraud.
No cross-track item has been Validated through end-to-end integration testing.
Generative AI status remains Not Confirmed.
ML Engineering pipeline and API are functional, but model recall on the risk class is only 0.04. Predictions are not production-ready.
Data Analytics is Confirmed at partial integration readiness.
Data Science is Reviewed (public GitHub repository).
This submission does not constitute a production banking system.
No personalized financial, investment, or legal advice is provided.

Section 13 — Conclusion

Week 4 concludes the FinTrust Digital Bank Experience Lab for the Project Management track. Across four weeks, the PM track has produced a complete governance foundation: charter, WBS, timeline, dependency register, risk register, issue log, decision log, and an evidence-based Integration Readiness Tracker with four-level hierarchy.

In Week 4, direct contributor communication upgraded two tracks to Confirmed level. Data Analytics is Confirmed at partial readiness (Franklin and Mohammed Rashid). ML Engineering is Confirmed at partial readiness (Dineo Nadine Sithole), with the pipeline and API functional and a documented model quality limitation (recall 0.04). Data Science remains Reviewed. Generative AI remains Not Confirmed.

Ten risks were closed, three accepted, two open. All issues classified. All dependencies documented. The individual presentation is recorded and reflects the full four-week contribution.

This Week 4 submission, along with Weeks 1 through 3, is maintained at https://github.com/LamSa1/FinTrust-PM-Portfolio.
